Pradhan Mantri Awas Yojana (PMAY-U)



Proposal for 2 projects under vertical AHP and 67 Projects under vertical BLC

Presented to 38th CSMC held on 26.09.2018

Government of Andhra Pradesh

PROGRESS OF PMAY (U)



Indicators	Current Status (No.)
■ Cities Approved	110
■ Demand Survey Completed	110
■ Total Demand	13,91,663
■ Demand received through Common Service Centre and Online Application	13,86,032
■ Cases accepted/rejected	
■ Whether HFAPoA Submitted	Yes
■ Whether AIP Submitted	Yes
■ Whether HFAPoA & AIP entered in MIS	Under Process
■ SLTC/CLTC staffs approved vs. placed	SLTC Placed . CLTC placed for 59 ULBs.
■ Target of DUs in 2018-19	7,09,930
■ State Budgetary Provision for PMAY (U) in 2018-19	893.382 Cr



STATUS OF MANDATORY CONDITIONS

Mandatory conditions	Current Status
■Dispensing the need for separate Non Agricultural (NA) Permission	Dispensed with vide G.O. Ms No. 98 dt. 19.02.2018 Revenue (DA & LR) Dept.
Prepare/amend their Master Plans earmarking land for Affordable Housing	Under process
Single-window, time bound clearance for layout approval and building permissions	Online permissions is in place
Adopt the approach of deemed building permission and layout approval on the basis of pre-approved lay outs and building plans.	Plan approvals exempted for BLC vide GO MS No. 405 Dt. 17.11.2017 MAUD (H) Dept.
Amend or legislate existing rent laws on the lines of the Model Tenancy Act.	Under process
Additional Floor Area Ratio (FAR)/Floor Space Index (FSI)/ Transferable Development Rights (TDR) and relaxed density norms.	Under consideration

INTERFACE WITH MIS



Indicators	Current Status (No.)
■Survey entry made (%)	98
■Projects approved:	353 (191 - AHP & 162 -BLC)
■Projects entered (7A/B/C/D)	333 (7B- 187 7C- 146)
■DUs approved under BLC	2,56,054
■Beneficiaries attached	1,64,131
■Houses geo-tagged	1,39,343 (BLC) and 1 <i>54</i> AHP Projects
■Total fund transferred through DBT (Rs. Lakhs)	1234.330 Cr (97,459 beneficiaries)
■National Electronic Funds Transfer (NEFT)	-
■PFMS/ DBT	-
■Aadhar Payment Bridge (APB)	1234.330 Cr

PROGRESS OF PROJECTS



V. P. L	Houses Work			Grounded/In Progress						
Verticals	ed	Tendered	orov Tendered	Approv Tendered order ed Issued	Issued	Foundation	Lintel	Roof	Total	Completed
■ISSR	-	-	-	-	-		-	-		
■AHP	5,19,910	4,60,492	4,60,492	2,36,123	=	85,733	3,21,856	32,639		
■BL-C (New)	2,56,054	-	1,44,792	36,605	-	10,609	47,214	50,741		
■BLC (Enhancement)										
Total	7,75,964	4,60,492	6,05,284	2,72,728	-	96,342	3,69,070	83,380		
■CLSS	No. of lo sanctione		-	-						

PROGRESS OF BLC PROJECTS



SI. NO	Details	2016-17	2017-18	2018-19	Total
1	Sanctioned	73,041	1,26,939	31,050	2,31,030
2	Finally taken up	31,401	1,26,939	31,050	1,89,390
3	Not Started	0	60,385	31,050	91,435
4	Houses Grounded	31,401	66,554	0	97,955
5	In progress	6,728	40,486	0	47,214
6	Completed	24,673	26,068	0	50,741

PROGRESS OF BLC PROJECTS




SI. NO	Details	2016-17	2017-18	2018-19	Total
ı	Utilisation of Funds Rs.	in Crores			
1	Central share utilised	345.88	394.72	0.00	740.60
2	State Share utilised	230.58	263.15	0.00	493.73
3	Total funds utilised	576.46	657.87	0.00	1234.33
II	Ist instalment of Centra	al share (40%	5)		
1	Approved	438.25	761.63	186.30	1386.18
2	Released	291.96	397.09	0.00	689.05
3	Balance to be released	146.29	364.54	186.30	697.13

- 1. Expenditure against Central share is Rs. 740.60 crs, but GoI released Rs. 689.05 crs. only.
- 2. Ist instalment of Central Assistance may be released, without any pre condition (i.e mapping of beneficiary data in PMAY MIS), as is being done in case of PMAY (Gramin)

WORK PROGRESS PHOTOS



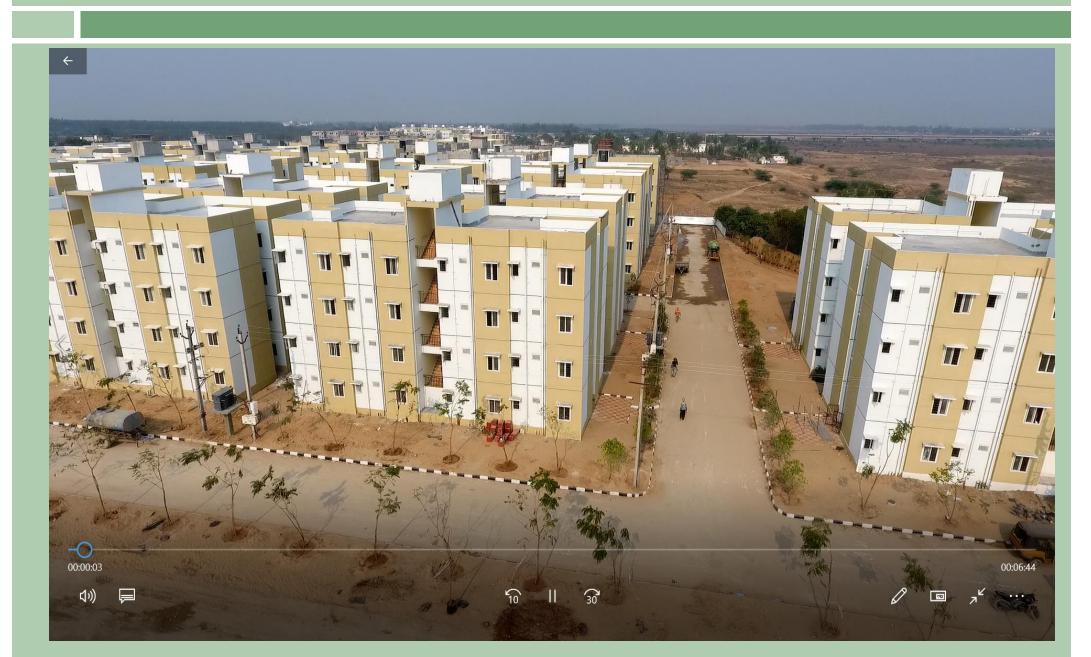























PROJECT PROPOSAL BRIEF



Verticals	ISSR	AHP	BLC (New)	BLC (E)	Remarks
■No. of Projects	-	2	67	-	
■No. of DUs	-	8,976	1,31,583	-	
■Project Cost	-	599.569 Cr	3323.265Cr	-	
■Central Share	-	134.640 Cr	1973.745Cr	-	
■State Share	-	134.640 0Cr	674.760 Cr	-	
■ULB Share (External Infrastructure)	-	83.982 Cr	-	-	
■Beneficiary Share	-	246.306 Cr	674.760 Cr		

Verticals (Rs. Lakhs)	Per Unit Cost	Central Share	State Share	ULB Share (External Infrastructure)	Benf. Share	Completion Time
■ISSR	-	-	-	-	-	-
■AHP	7.7 Lakh	1.50 Lakh	1.50 Lakh	83.982 Cr	3.77 Lakh	24 months
■BLC (N/E)	3.50 Lakh	1.50 Lakh	1.00 Lakh	-	1.00 Lakh	12 months
■ UDAs (BLC)	2.50 Lakh	1.50 Lakh	0.50 Lakh	-	0.50 Lakh	12 months

PROJECT PROPOSAL BRIEF



Checklist	Status (Y/N)
■Layout plan(as per NBC norms) Attached	Υ
■SLAC/SLSMC approval/Minutes submitted	Υ
■Land title status (encumbrance free)	Υ
■Beneficiary list (BLC) submitted	Υ
■No. of Beneficiaries with Aadhar ID	1,40,559
■No. of Beneficiaries with other Unique ID	-
■No. of Aadhar seeded Bank accounts	1,40,559
■Status of physical & social infrastructure	Proposed in DPRs
Implementation plan/Completion period	24 /12 Months
Beneficiary consent sought	Υ

ROAD MAP



Sl.No	Financial Year	Sanction of Houses	Completion of Houses
1	2015-16 (Actual)	1,93,147	0
2	2016-17 (Actual)	0	1,860
3	2017-18 (Actual)	4,88,586	40,146
4	2018-19	7,09,930	2,14,478
5	2019-20	0	4,00,000
6	2020-21	0	4,57,994
7	2021-22	No Sanctions for this year and	2,77,185
		left for only completion.	
	TOTAL	13,91,663	13,91,663*
	*Demand Survey S to be revised	Status to be completed in UDAs a	nd total Demand need



BEST PRACTICE/INNOVATION

Innovative technology Adopted - Shear wall Technology in AHP Details of IEC initiatives — Workshops, pamphlets, banners highlighting the PMAY (Urban) Program.



Thanking You
