

### Pradhan Mantri Awas Yojana (PMAY) Housing For All (Urban) Mission

48<sup>TH</sup> CENTRAL SANCTIONING AND MONITORING COMMITTEE (CSMC)
MEETING

Date : 31st October 2019

Venue: : Nirman Bhawan, New Delhi.



Presented by:

MUNICIPAL AFFAIRS DEPARTMENT
GOVERNMENT OF NAGALAND
[State Level Nodal Agency for PMAY – HFA (U)]

### Progress of PMAY (U)

Indicators	Current Status (No.)
■ Cities Approved	32 Towns
■ Demand Survey Completed	32 Towns
■ Total Demand Assessment (till date)	30,921
■ Whether HFAPoA Submitted	Yes (32 Towns)
■ SLTC /CLTC staffs approved vs placed	• SLTC (9/9) • CLTC (28/28)
■Projects approved under BLC (N/E)	47 Projects
■ DU's approved under BLC	27, 683

### **Progress of Projects**

Mauticala	als Houses Tender Approved floated	Tender	Work	Gro	Canadatad			
Verticals		order issued	Found ation	Lintel	Roof	Total	Completed	
■ ISSR	-	-	-	-	-	-	-	-
■ AHP	-	-	-	-	-	-	-	-
■ BLC (N/E)	27,683	-	16123	5,931	1,272	405	7,608	408
■ Total	27,683	-	16123	5,931	1,272	405	7,608	408
- CLSS	23							


### **Proposals**

- 1) 8 BLC NEW HOUSE PROJECT DPRs
- 2) 6 BLC ENHANCEMENT PROJECT DPRs
- 3) Cancellation of BLC ENHANCEMENT PROJECT FOR SHAMATOR TOWN

### Proposal 1: BLC-New House Projects Proposal

			Project Cost								
SI. No.	Town	Total Number of Beneficiaries	GOI Share In Lakhs	State Share In Lakhs	ULB Share (Rs. in Lakhs)	Beneficiary Share (Rs. in Lakhs)	Total (Rs in Lakhs)				
1	Aboi	566	849.000	0.000	0.000	1471.600	2320.600				
2	Longkhim	209	313.500	0.000	0.000	589.380	902.880				
3	Chozuba	437	655.500	0.000	0.000	1241.080	1896.580				
4	Meluri	309	463.500	0.000	0.000	889.920	1353.420				
5	Pfutsero	717	1075.500	0.000	0.000	2036.280	3111.780				
6	Tenning	209	313.500	0.000	0.000	537.130	850.630				
7	Tizit	396	594.000	0.000	0.000	1015.344	1609.344				
8	Tobu	150	225.000	0.000	0.000	390.000	615.000				
	TOTAL	2993	4489.500	0.000	0.000	8170.734	12660.234				


**Note**: The Central Share comprises of Central Subsidy of Rs. 1.50 Lakhs per beneficiary released in 3 Installment – 40%, 40% & 30% depending on the stages/level of Construction. The remaining cost of DU is to be borne by the beneficiaries themselves.

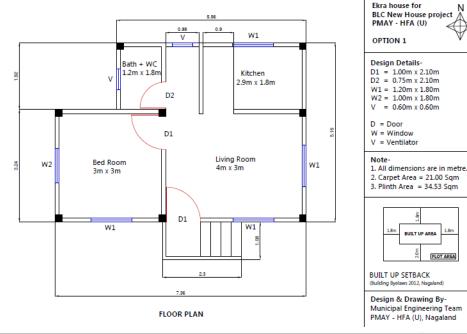






(New House: Option-I)




(New House: Option-II)

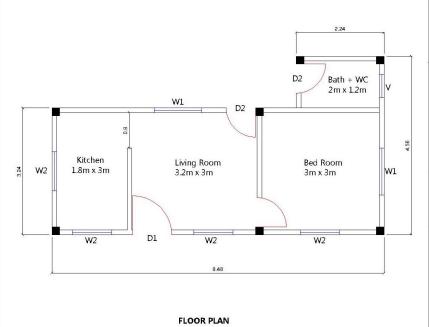

**Design For BLC New House** PMAY - HFA (U) **OPTION 2** Design Details- $D1 = 1.00 \text{m} \times 2.10 \text{m}$  $D2 = 0.75 \text{m} \times 2.10 \text{m}$  $W1 = 1.20 \text{m} \times 1.80 \text{m}$  $W2 = 1.00 \text{m} \times 1.80 \text{m}$  $V = 0.60 \text{m} \times 0.60 \text{m}$ D = Door W = Window V = Ventilator Note-1. All dimensions are in metre. 2. Carpet Area = 26.40 Sqm

- 3. Plinth Area = 30.43 Sqm




BUILT UP SETBACK (Building Byelaws 2012, Nagaland)

Design & Drawing By-Municipal Engineering Team PMAY - HFA (U), Nagaland

- •. 2 options of Floor Plan is provided in the DPR for BLC-NHC Project.
- Options for 2 kinds construction technology – Ekra Wall & Wooden House, besides Brick Walling are provided

**Layout Plan** For **BLC-New House** 

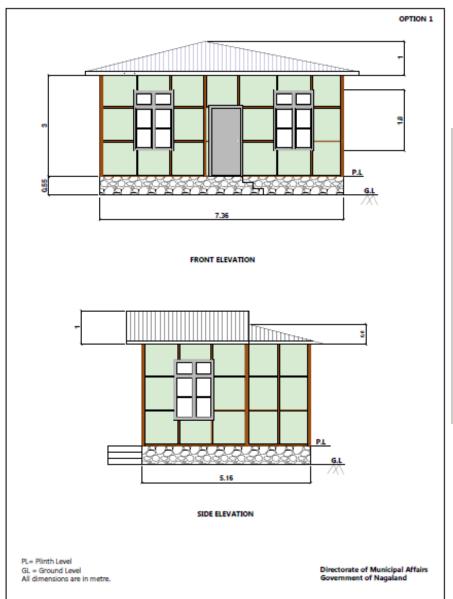





Elevations & View of Ekra Wall BLC- New House

### **EKRA WALL HOUSE Technology: Wall Framing**






TYPE 1A with 3 nos. vertical bamboo split




Note:	
TYPE 1A	TYPE 1B
Frame size = 3'x3' Timber size = 3"x4" Bamboo split = 2'-6"x1"	Frame size = 3'x3' Timber size = 4"x3" Bamboo split = 2'-4"x1"






TYPE 2A with 4 nos. vertical bamboo split




TYPE 2B with 4 nos. vertical bamboo split

lote :	
TYPE 2A	TYPE 2B
Frame size = 3'x3' Timber size = 3"x4" Bamboo split = 2'-6"x1"	Frame size = 3'x3' Timber size = 4"x3" Bamboo split = 2'-4"x1"





Type 1 Bamboo split walling plan

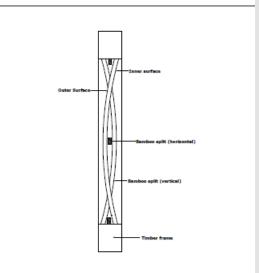

Type 2 Bamboo split walling side elevation

\*Not in scale

### **EKRA WALL HOUSE CONSTRUCTION**


















### **WOODEN HOUSE**

### **Reasons for Adoption**

It is cheaper as it significantly reduces the transportation cos of carrying other materials such as bricks, cement and othe materials used in RCC structures etc
☐ It is locally available as most beneficiaries opting for wooder house have their own resource of wood and thus reduces the cost o
buying building materials
$oldsymbol{\square}$ The construction process is faster as well as less labo intensive.
☐ Timber also offers sustainability benefits, as it comes from renewable source (as long as it is replanted, it will continue to be available)
☐ Reduces on-site waste in comparison to other construction materials.

### WOODEN HOUSE: Construction Method & SPECIFICATIONS

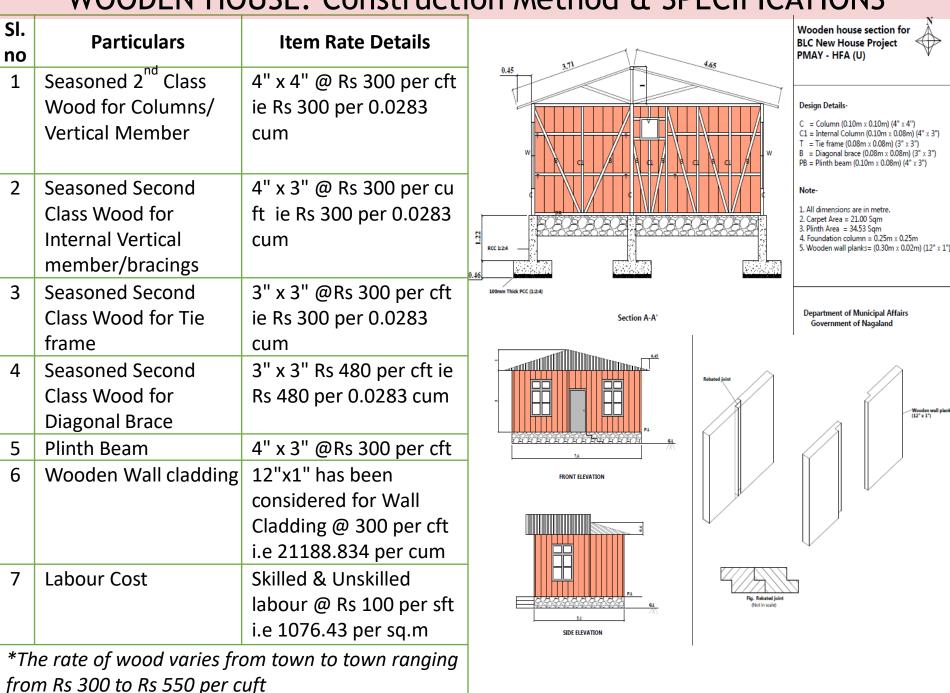










Wooden Houses constructed under BLC-New House, Shamator Town


### Proposal 2: BLC-Enhancement Projects Proposal

			Project Cost							
Sl. No.	Town	Total Number of Beneficiaries (Enhancement)	GOI Share	State Share	ULB Share (Rs. In Lakhs)	Beneficiary Share (Rs. in Lakhs)	Total (Rs. In Lakhs)			
1	Aboi	4	6.000	0.000	0.000	3.214	9.214			
2	Chozuba	42	63.000	0.000	0.000	45.926	108.926			
3	Meluri	29	43.500	0.000	0.000	36.483	79.983			
4	Pfutsero	120	180.000	0.000	0.000	228.379	408.379			
5	Tening	37	55.500	0.000	0.000	82.054	137.554			
6	Tizit	13	19.500	0.000	0.000	14.922	34.422			
	TOTAL	245	367.500	0.000	0.000	410.979	778.479			

### OPTIONS OF PLAN UNDER BLC - ENHANCEMENT

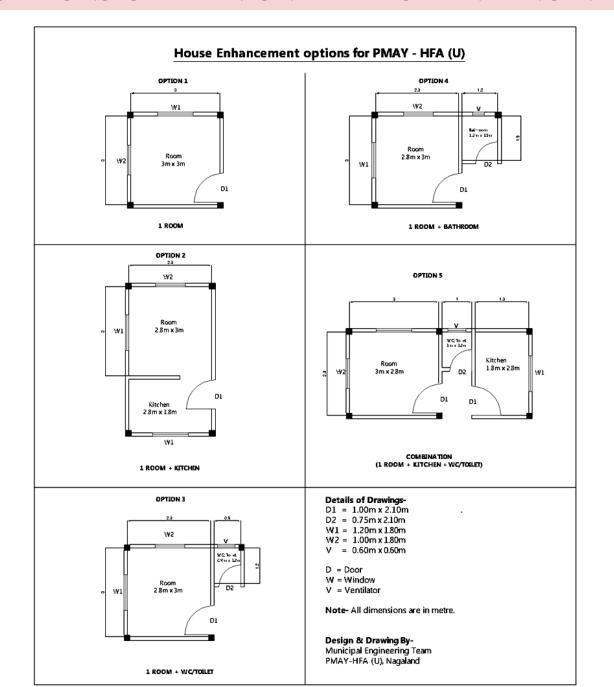

#### 3D VIEW OF OPTIONS UNDER BLC - ENHANCEMENT

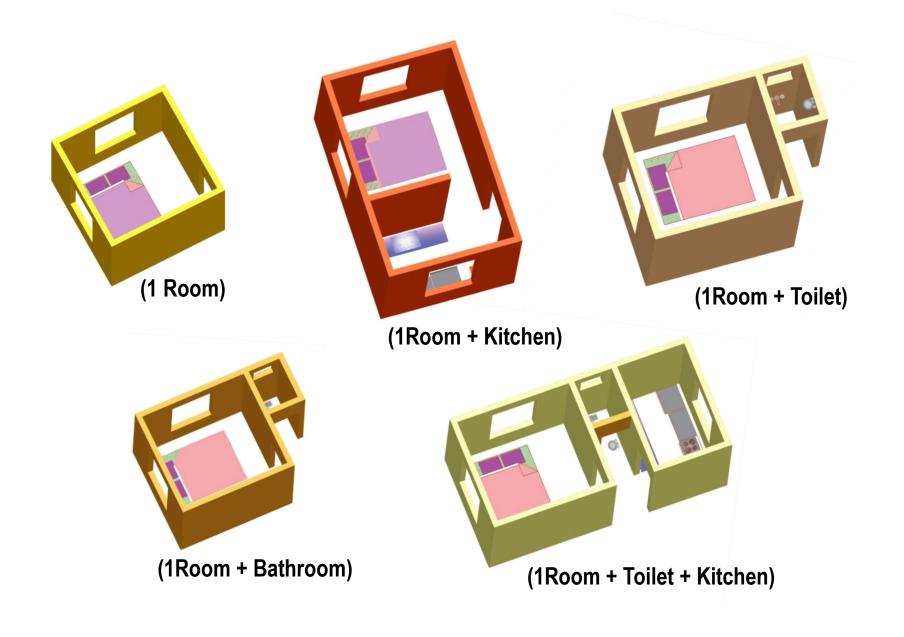

# Proposal 3: Cancellation of BLC Enhancement Project for Shamator Town

- 1. On physical verification of the beneficiaries' houses who have applied under BLC Enhancement, it was found that all the 275 beneficiaries applied for enhancement of rooms were owning kutcha house and therefore not eligible for enhancement but eligible for New House Construction.
- 2. As per Ministry's SOP on MIS, modification/replacement cannot be made once attached to the DPR in the MIS portal from the SLNA but with proposal of the SLSMC for curtailment of ineligible/wrongly entered beneficiaries or cancellation of such projects.
- 3. The beneficiaries eligible for New House is required to be proposed under a new DPR for BLC NEW House.


### MIS Progress & Geotagging Status as on 30/10/2019

Project	DU's Approved	Uploaded	Attached	Geo-tagged	Under Construction	Completed
BLC New House	16,542	15,733	12,732	11,258	4,133	30
BLC - Enhancement	11,141	10,151	8,490	7,341	3,475	74
Total	27,683	25,884	21,222	18,599	7,608	104
Percentage (%)		93.50%	76.66%	67.18%	27.48%	*0.38%

<sup>\*</sup>Percentage against the total DU approved

\* The number of completed houses on ground is between 500-600 DUs. However, some final stage geo-tagged points are yet to be accepted while some are rejected during moderation for poor photography quality, while many points are not appearing in the Bhuvan portal despite being sent by the surveyors.

### MIS Progress & Geotagging Status as on 30/10/2019

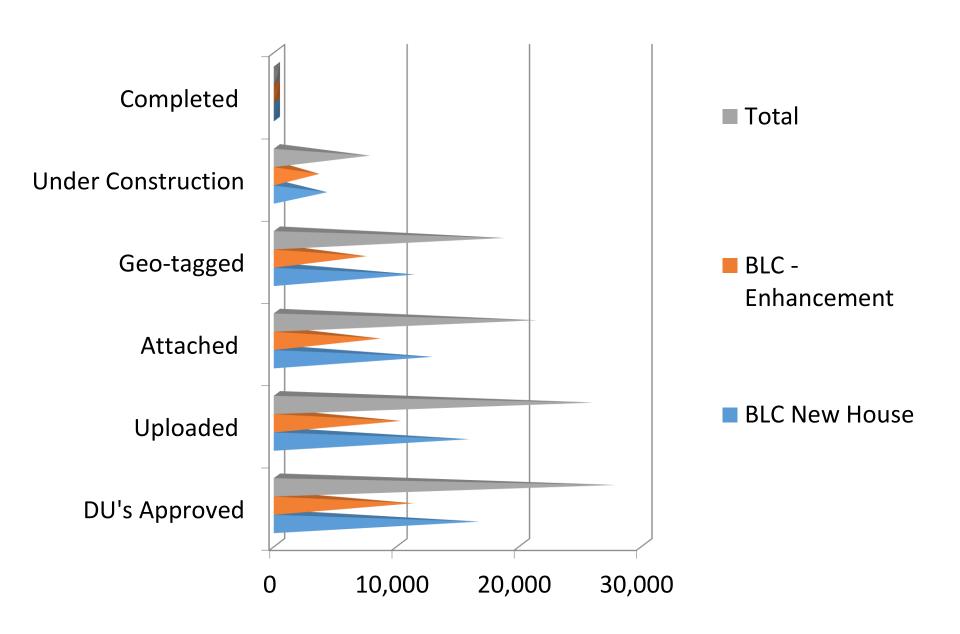

### Financial Progress/ Fund Disbursement as on 30/10/2019

Total Sanctio	n by Ministry	Total F	Released by SLNA	
Amount (in Lakhs)	Number of Beneficiaries	Amount (in Lakhs)	Number of Beneficiaries	%
12675.60	21126	8829.60	14716	70%

ilization Certificate Submitted	Rs. 5844.80 Lakhs (46%)
---------------------------------	-------------------------

### Status of Credit Linked Subsidy Scheme

	Name of Towns					6 1 11	_
Name of PLI	Chumuke- dima	Dima- pur	Kohi -ma	Mokokc- hung	Total	Subsidy Claim	Income Category
Allahabad Bank				1	1	1	EWS
Bank of Baroda		1			1	1	LIG
Bank of Maharashtra		1			1	1	EWS
Canara Bank			2		2	2	2 MIG-I
Indian Bank		4			4	4	2 LIG, 2 MIG-I
UCO Bank		1	5		6	6	All MIG-I
United Bank of India		3			3	3	I EWS, 2 LIG
Vijaya Bank	1	1	3		5	5	1 EWS, 4 LIG
<b>Grand Total</b>	1	11	10	1	23	23	

**Note**: The number of loans disbursed is more than 30 however interest subsidy yet to be claimed by the PLIs from the CNS and therefore is not entered in the MIS portal

Glimpses of Completed Houses, Ongoing different Levels of Construction of Houses under BLC Projects of PMAY-HFA(U) in Nagaland



Name of Beneficiary: Rajan Chetri



**BLC - New House Construction in Kohima Town** 



**NAME: - SANJAY KUMAR CHETTRI** 



**BLC - New House Construction in Kohima Town** 



NAME OF BENEFICIARY: VIKEHIEKHO KINTSO



**BLC - New House Construction in Kohima Town** 

#### NAME: - Nzanbemo Lotha Component: ENHANCEMENT



**BLC HOUSES Constructed in Dimapur Town** 

NAME: - - Nzilo

**Component: ENHANCEMENT** 









**BLC HOUSES Constructed in Dimapur Town** 

#### **NAME: - Zubeni Ovung**



#### **Component: ENHANCEMENT**







**BLC HOUSES Constructed in Dimapur Town** 

#### **NAME: - Pithungo Ngullie**





**BLC HOUSES Constructed in Dimapur Town** 

NAME: - AKUH K Component: NEW HOUSE





**BLC HOUSES Constructed in Mon Town** 

#### Name: TONPHA KONYAK Component: NEW HOUSE





**BLC HOUSES Constructed in Mon Town** 

#### **NAME: - LONGTSUBENI LOTHA**

#### **Component: NEW HOUSE**



**BLC HOUSES Constructed in Wokha Town** 

#### **NAME: - MYANLUMI NGULLIE**

**Component: NEW HOUSE** 



**BLC HOUSES Constructed in Wokha Town** 

#### **NAME: - MHABENI SHITIRI**

#### **Component: ENHANCEMENT**



**BLC HOUSES Constructed in Wokha Town** 





Wooden Houses constructed under BLC - New Houses, Shamator Town



Wooden Houses constructed under BLC - New House at Kiphire Town







Pucca Houses constructed under BLC - New House at Kiphire Town







Name: Toshuli Achumi

Location: Ward 22,

**Dimapur Town** 

Name: Lujikiu

Location: Ward 22,

**Dimapur Town** 





Name: Mughase Muru

Location: Ward 22,

**Dimapur Town** 

Name: Willto Aye Location: Ward 22, Dimapur Town



## THANK YOU
