Pradhan Mantri Awas Yojana (PMAY-U)



Government of Karnataka

SLNA: Rajiv Gandhi Housing Corporation Ltd.

PROGRESS OF PMAY (U)



TROUNDER (C)						Pradhan Mantri	Awas Yojana-Urban
Indicators	Current Status (No.)			(No.)			
■ Cities Approved	275						
■ Demand Survey Completed	Completed in 271 ULBs. Demand survey will be commenced in newly upg 4 cities.			y upgro	aded		
■ Total Demand	19.01 Lakhs (validated 12.54 lakhs)						
Demand received through CSC & Citizen portal	CSC: 2.63 Lakhs & Citizen portal: 5.91 Lakhs						
Cases accepted/rejected		Source	Received	Accepted	Rejected	Pending	
' / '		ULB	10.41	10.41	0		0
		Citizen	5.92	1.49	1.92	2.	.49
		CSC	2.62	.66	1.11	0.	.84
		Total	19.00	12.54	2.96	3.	.34
Whether HFAPoA Submitted		•	ections of Tender ha	•		are	being
■ Whether AIP Submitted	AIP will be submitted after approval of HFAPoA						
Whether HFAPoA & AIP entered in MIS	Will be updated after approval of Gol						
■ SLTC/CLTC staffs approved vs. placed	SLTC: 10 / 5 & CLTC:128 / 110						
■ Target of DUs in 2019-20	As per Road map submitted – 3,50,000						

INTERFACE WITH MIS



Indicators	Current Status (No.)
■Survey entry made (%)	12.54 Lakhs
■Projects approved:	1831
■Projects entered (7A/B/C/D)	1748
■DUs approved under BLC & AHP	BLC: 179158 (1477 Projects) AHP: 355461 (354 Projects)
■Beneficiaries attached	BLC: 140055 (83.14%); AHP:141375 (40%) Total: 281430 (52%)
■Houses geo-tagged	BLC: 122219 (72.55%), AHP: 190
■Total fund transferred through DBT (Rs. Lakhs)	833.23 Crores
■National Electronic Funds Transfer (NEFT)	739.07 Crores
■PFMS/ DBT	0
■Aadhar Payment Bridge (APB)	94.154 Crores



PROGRESS OF PROJECTS

			Work order Issued	Grounded/In Progress					
Verticals	Houses Approved	Tendere d		Foundat ion	Lintel	Roof	Total	Complete d	
ISSR	Nil	0	0	0	0	0	0	0	
AHP	3,55,461	1,44,709	1,23,819	22,840	7,112	14,009	43,961	8,846	
BLC (New)/Enhan cement	1,79,158	1,14,039	1,40,322	12,443	12,760	14,250	39,453	90,683	
■Total	5,34,619	2,58,748	2,64,141	35,283	19,872	28,259	83414	99,529	
■ CLSS	No. of sanctio			35,883					

PROJECT PROPOSAL BRIEF



					(Rs. In lakh)
Verticals	ISSR	AHP	BLC (New)	BLC (E)	Remarks
■No. of Projects	0	7	283	1	
■No. of DUs	0	810	29967	95	
■Project Cost	0	5716.32	120256.50	159.60	
■Central Share	0	1215.00	44950.50	142.50	
■State Share	0	1935.50	18207.60	0.00	
■ULB Share	0	1152.72	0.00	0.00	
■Beneficiary Share	0	1413.10	57098.40	1 <i>7</i> .10	

Verticals (Rs. Lakhs)	Per Unit Cost	Gol Share	State Share	ULB Share	Benf. Share	Completion Time
■ISSR	NA	NA	NA	NA	NA	NA
■AHP	5.00	1.5	1.20 for Gen 2.00 for SC/ST	0	2.30 for Gen 1.50for SC/ST	NA
■BLC-New	4.00	1.5	1.20 for Gen 2.00 for SC/ST	0	1.30 for Gen 0.50 for SC/ST	18 months
■ BLC- Enhancement	NA	NA	NA	NA	NA	NA

^{*} Includes bank loan too



PROJECT PROPOSAL BRIEF

Checklist	Status (Y/N)
■Layout plan(as per NBC norms) Attached	Yes
SLAC/SLSMC approval/Minutes submitted	SLAC proceedings submitted
■Land title status (encumbrance free)	Yes
■Beneficiary list (BLC) submitted	Yes
■No. of Beneficiaries with Aadhar ID	BLC:
■No. of Beneficiaries with other Unique ID	0
■No. of Aadhar seeded Bank accounts	BLC:
■Status of physical & social infrastructure	BLC: infrastructure already exists
Implementation plan/Completion period	BLC:18 months
■Beneficiary consent sought	Yes



STATUS OF MANDATORY CONDITIONS

Mandatory conditions	Current Status
Dispensing the need for separate Non Agricultural (NA) Permission	Completed
■Prepare/amend their Master Plans earmarking land for Affordable Housing	Under Process
■Single-window, time bound clearance for layout approval and building permissions	Under Process
Adopt the approach of deemed building permission and layout approval on the basis of pre-approved lay outs and building plans.	Under Process
Amend or legislate existing rent laws on the lines of the Model Tenancy Act.	Under Process
•Additional Floor Area Ratio (FAR)/Floor Space Index (FSI)/ Transferable Development Rights (TDR) and relaxed density norms.	Under Process

Thank You

Photo Gallery PMAY – Urban (AHP Houses)

Construction of 3630 Houses under PMAY (U) in Gadag-Betagreri, Gadag District







Construction of 1152 (G+2)Houses under PMAY (U) in Dandeli, Uttara Kannada District







Construction of 504 (G+2) Houses under PMAY (U) Haliyala, Uttara Kannada District



Construction of 1303 Houses under PMAY (U) Arasikere, Hassan District








Construction of 500 (G+2)Houses under PMAY (U) in Basavana Bagewadi, Vijayapura Dist







Construction of 917 Houses under PMAY (U) Kanakapura, Ramanagara District

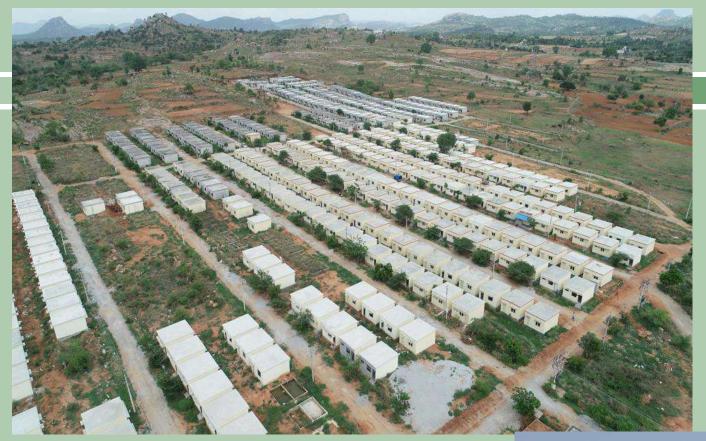



Construction of 204 Houses under PMAY (U) in Siggon ULB, Haveri District



Construction of Houses by KSDB under PMAY (U) in Vijayapura, Vijayapura District



Construction of Houses by KSDB under PMAY (U) in Vijayapura, Vijayapura District



CONSTRUCTION OF GROUP HOUSES IN GUNDLUPET (CHAMARAJANAGAR DIST) PKGB





Photo Gallery PMAY – Urban (BLC Houses)

Belgaum dist Kallolli ULB



















BLC House photos









Photo Gallery PMAY – Urban CLSS

Meeting with Bankers on CLSS under chairmanship of MD, RGHCL

26











Meeting with Bankers on CLSS under chairmanship of Lead Bank Manager, Kalaburgi



28







CLSS Home Ioan Mela- Haveri









CLSS Home Ioan Mela- Haveri









CLSS Home Ioan Mela- Dharwad



CLSS Home Ioan Mela- Dharwad



Orientation Programme on CLSS. Nelamangala



CLSS Home Ioan Mela- Kodathi, Bangalore



Photo Gallery PMAY – Urban Meetings & Workshops

Progress review on Central Sponsored Schemes by Secretary, MoHUA



Workshop on PMAY (U) MIS and Nomination of PMAY Award

