



# PROPOSAL FOR 37 BLC PROJECTS IN JHARKHAND



**Urban Development and Housing Department**

**Government of Jharkhand**

**Date : 21<sup>th</sup> March, 2017**




# Progress of BLC projects

Total no. of approved Project	: 108
No. of Beneficiary	: 40,486
Total Project Cost	: 1466.00 Cr.
Total GoI Share	: 607.29 Cr.
Total GoJ Share	: 303.65 Cr.
Beneficiary Share	: 555.06 Cr.

## Progress of approved units (40,486) till Date

Completed Units	: 778
Units in progress	: 30,206
Total	: 30,984 (76.53%)

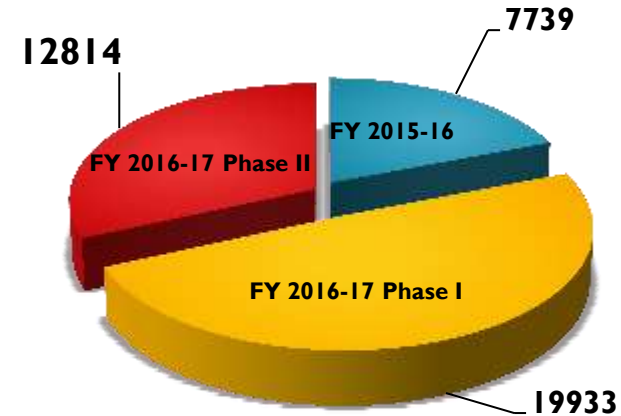

Approved DUs 40,486

■ 4th CSMC ■ 12th CSMC ■ 14th CSMC

# Progress of BLC projects


## Approved in 4th CSMC meeting

Total no. of approved Project : 39

No. of Beneficiary : 7,739 (Revised)

### Progress of approved units (7,739) till Date

Agreement	: 7,682
Foundation	: 1,773
Plinth	: 2,705
Roof	: 2,320
Completed	: 674

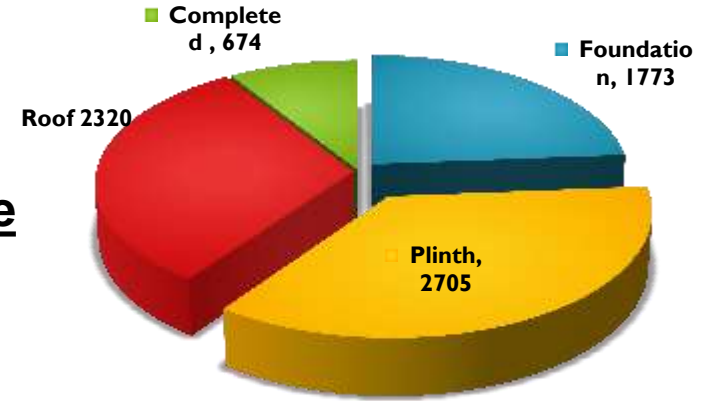

**Approved DUs 7,739**

■ Foundation ■ Plinth ■ Roof ■ Completed

# Progress of BLC projects


## Approved in 12th CSMC meeting

Total no. of approved Project : 33

No. of Beneficiary : 19,933

## Progress of approved units (19,933) till Date

Agreement	:	19,310
Foundation	:	11,896
Plinth	:	1,950
Roof	:	324
Completed	:	3

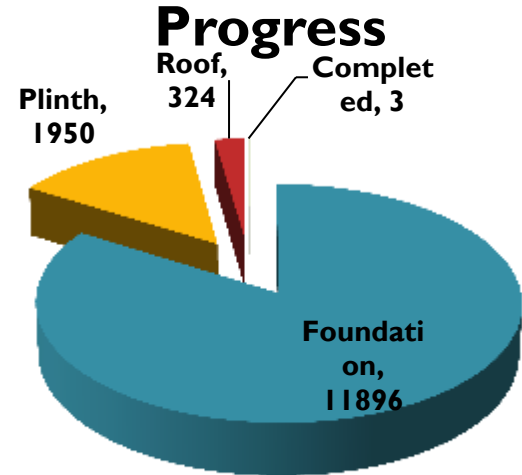

■ Foundation ■ Plinth ■ Roof ■ Completed

[Progress Details](#)

# Progress of BLC projects


## Approved in 14th CSMC meeting

Total no. of approved Project : 36

No. of Beneficiary : 12,814

### Progress of approved units (12,814) till Date

Agreement	:	12,452
Foundation	:	6,326
Plinth	:	1,517
Roof	:	395
Completed	:	101

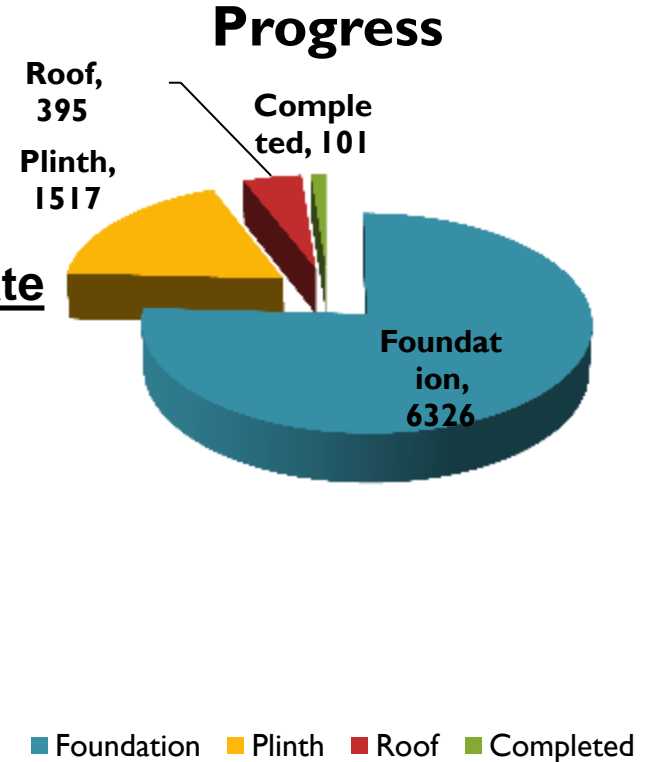

## Action initiated at State Level

PMC appointed for monitoring and supportive supervision of construction of DUs

Ward wise work distribution for monitoring of construction among ULB officials

Validation of online application received through CSC SPV & PMAY- MIS portal is in process. Total no. of applications validated 12,255 and Total no. applications approved 11,572.

Recruitment for SLTC and CLTC (total 62 positions) is under process.

2078 application forms have been submitted to banks for loan approval. Bank wise information has been shared with GOI

HFAPoA completed of all ULBs after incorporating the feedback from GOI

## Contd..

Annual Implementation Plan preparation is under process. It will be submitted to GOI before 2<sup>ND</sup> week of April 2017.

Public Grievance Management System has been launched.

Supervisors (73) and surveyors (122) have been nominated at each ULBs for field data collection.

State Level Inspection and Monitoring committee constituted at Directorate level to monitor the progress of work.

22,109 DUs have been Geo Tagged till date.

RFP prepared for construction of 40000 DUs using new and emerging Technologies across the state.



# Glimpses of Dwelling Units (BLC)

Pusro, Bokaro



लाभुक : संदीप रजक, वार्ड नं० : 26, नगर परिषद, फुसरो



प्रधानमंत्री अवास योजना 2015-16

सुरेश महतो  
वार्ड नं० : 15



लाभुक : अनिता देवी, वार्ड नं० : 23, नगर परिषद, फुसरो

# Glimpses of Dwelling Units (BLC)

## Chaibasa





# Glimpses of Dwelling Units (BLC)

## Pakur



# Glimpses of Dwelling Units

## Bundu



# Glimpses of Dwelling Units

## Gumla





# Glimpses of Dwelling Units



# Glimpses of Dwelling Units(Under Construction)





# Glimpses of Dwelling Units





# Geo Tag – 22100 DUs (till date)



Enter City or Lat, Lon



Arab Emirate

Oman

500 km


Bhuvan

[Tools](#) | [Link](#) | [Home](#) | [Help](#)

## Housing For All Asset DETAILS




Sl.No	192755
Beneficiary Name	SATYA BAURI
Project Name	Beneficiary-led Construction, Vertical: 4 - Chirkunda
Address	LAYAKDIH, LAIKDIH BAURI TOLA, Chirkunda, Jharkhand, Chirkunda Dhanbad Jharkhand

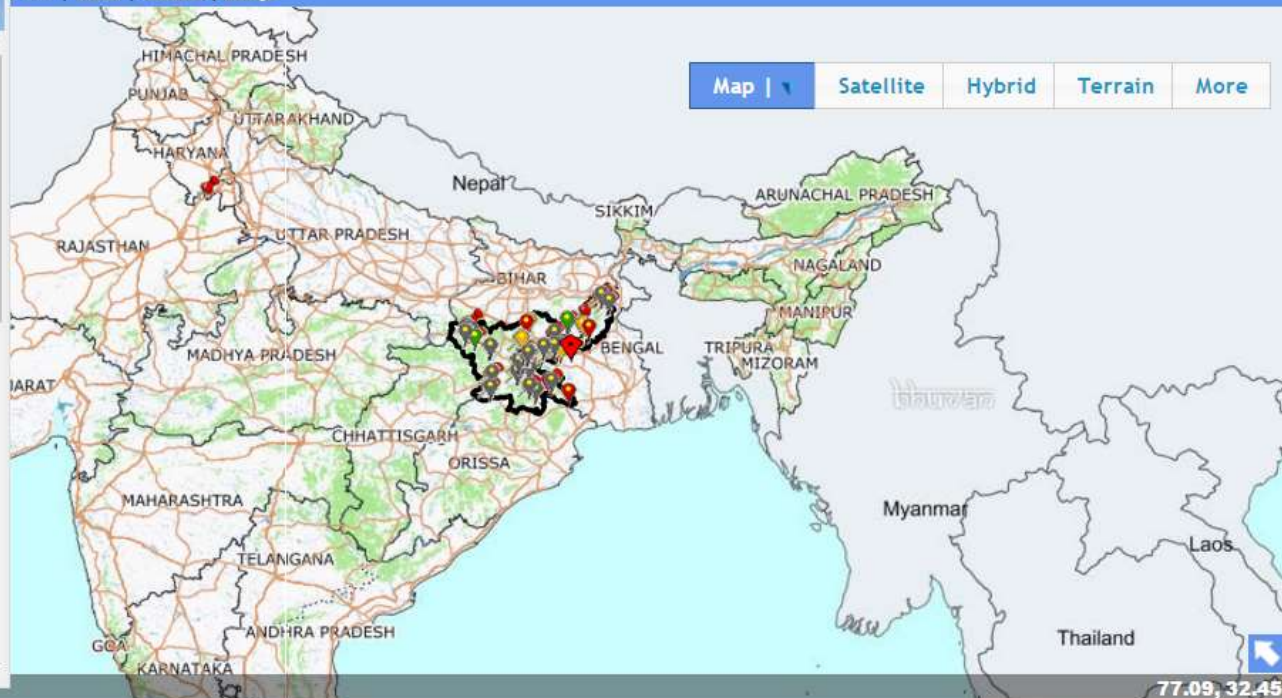

77.09, 32.45

# Geo-tagging Field Map

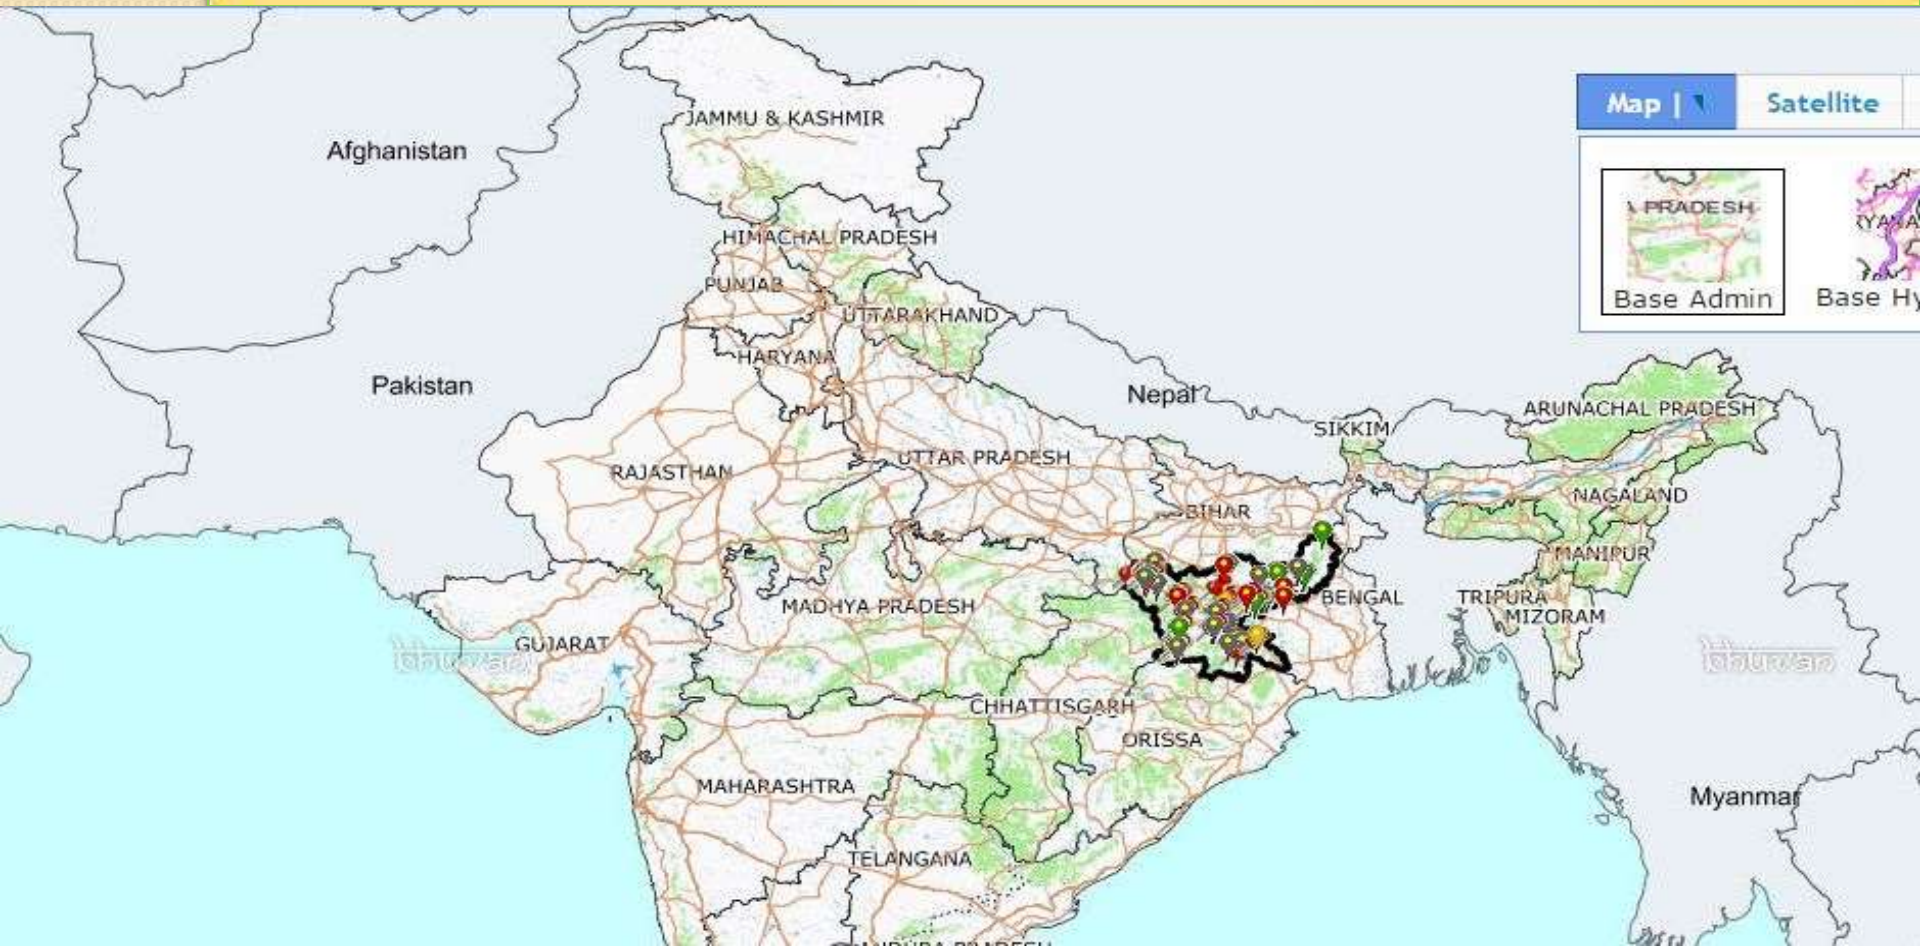



## Ministry of Housing and Urban Poverty Alleviation Housing for All

Welcome Jharkhand\_hfa [Logout](#)



[Tools](#) | [Link](#) | [Home](#) | [Help](#)

Map | Satellite | Hybrid | Terrain | More

JHARKHAND

Dumka

**Housing For All Asset DETAILS**

1 2

Sl.No	139787
Beneficiary Name	SNIGADHA DEVI
Project Name	Beneficiary-led Construction for Dumka Nagar Parishad
	178A, PARVATI GATE

10 km

# NRSC Report State Wise (PMAY-MIS Portal)



## NRSC Survey Report State wise

State Name :

Jharkhand

Show

### City Name : Hussainabad

S.No	Beneficiary Id	Beneficiary Name	Age	Project Name	Construction Stage	photo 1	photo 2
1	208017840334300003	fultush devi	44	Beneficiary-led construction vertical 4 111 Dus PMAY of Hussainabad ULB, Jharkhand	Foundation		
2	208017840334300006	karmi devi	52	Beneficiary-led construction vertical 4 111 Dus PMAY of Hussainabad ULB, Jharkhand	Foundation		



## NRSC Survey Report State wise

State Name :

Jharkhand

Show

### City Name : Adityapur (Nagar Parishad)

S.No	Beneficiary Id	Beneficiary Name	Age	Project Name	Construction Stage	photo 1	photo 2
1	208018010181900088	SUDHIR KUMAR MAHATO	45	Beneficiary-led Construction Vertical 4 of 1845 DUs under PMAY of Jamshedpur UA, Jharkhand.	Lintel		
2	208018010183900013	Dinesh Lohar	33	Beneficiary-led Construction Vertical 4 of 1845 DUs under PMAY of Jamshedpur UA, Jharkhand.	Lintel		





## NRSC Survey Report State wise

State Name :

Jharkhand

Show

City Name : Basukinath

S.No	Beneficiary Id	Beneficiary Name	Age	Project Name	Construction Stage	photo 1	photo 2
1	208017900419700019	Nawal Kishore Patralekh	50	Beneficiary led-construction Vertical 4, 83 DUs under PMAY of Basukinath ULB, Jharkhand	Roof		
2	208017900419900007	Kartik Rao	60	Beneficiary led-construction Vertical 4, 83 DUs under PMAY of Basukinath ULB, Jharkhand	Roof		


## NRSC Survey Report State wise

State Name :

Jharkhand

Show

City Name : Phusro (Nagar Parishad)

S.No	Beneficiary Id	Beneficiary Name	Age	Project Name	Construction Stage	photo 1	photo 2
1	208017770275800011	Satish Giri	23	Beneficiary Led Construction Vertical 4 of 381 DUs under PMAY of Phusro ULB, Jharkhand	Completed		
2	208017770275500006	Khusboo Devi	22	Beneficiary Led Construction Vertical 4 of 381 DUs under PMAY of Phusro ULB, Jharkhand	Completed		



# Awareness/ Stakeholders workshops

IEC campaign conducted in all ULBs

**प्रधानमंत्री आवास योजना**  
सबके लिए आवास (शहरी)

कारखान्ड सरकार का है सड़क बादा, हर परिवार को घर देने का है पक्का इरादा

नगर पूर्णता  
नगर आवासीय विकास  
मिश्रित नगर विकास  
शहरी आवासीय विकास



At India International Mege trade fair (IIMTF) Ranchi

# Awareness/ Stakeholders workshops

IEC campaign conducted in all ULBs

विश्वसनीय नगरीय विकास के लिए, हर परिवार को घर बनाने का अवसर देना

**प्रधानमंत्री आवास योजना**  
सबके लिए आवास (शहरी)

**नींव खुदाई सप्ताह**  
(26 जुलाई-01 अगस्त 2016)



उक्त दिवस में सभी नगर निकाय अपने-अपने क्षेत्रों में योजना अन्तर्गत चयनित लाभुकों के आवास के नींव खुदाई कर कार्य प्रारंभ करेंगे।

**चयनित आवास निर्माण (आर्थिक रूप से कमजोर वर्ग के लिए)**

- \* चयनित लाभुकों के आवास की नींव खुदाई
- \* चयनित लाभुकों को योजना की प्रथम किस्त की राशि का वितरण

आवक कार्य दिनांक पर दोपहर 3 बजे से शाम 5 बजे तक सम्पन्न करें - हेल्पलाइन नं. - 8661-6372777

“इसारेखंड सरकार का है वह बादा, हर परिवार को घर देने का है पक्का इरादा”

अधिक जानकारी के लिए सम्पर्क करें

स्थानीय नगर निकाय कार्यालय, नगर निकाय एवं आवास विभाग, इलाहाबाद

E-mail: jhanki@gnail.com, Website: http://mhpa.gov.in/pmay/index.html



Jhanki on Republic Day 2017



# Public Grievance Management System

आरक्षण का जवाबदार ना जवाब, का जवाब देना आरक्षण।  
 Baidk Bhaskar, Ranchi edition 20-12-16

## पोर्टल से जुड़ कर नगर विकास से जुड़ी परेशानी बताए शहरी आबादी: मंत्री लोग बिल्डिंग प्लान एप्रूवल के लिए ऑनलाइन दे सकते हैं आवेदन

किरी रिपोर्टर | संतो/हरिया

नगर विकास और आवास विभाग ने सोमवार को झारखंड अफोर्डेबल अर्बन हाउसिंग पॉलिसी, झारखंड वाटर यूजर चार्जिंग पॉलिसी 2016 फॉर अर्बन एरियाज और एडवर्टीजमेंट पॉलिसी फॉर अर्बन लोकल बॉडीज का विमोचन किया। मौके पर नगर विकास मंत्री सीपी सिंह ने दो पोर्टल फॉर्मिक ग्रीनबैज मैनेजमेंट सिस्टम और ऑनलाइन बिल्डिंग प्लान एप्रूवल मैनेजमेंट सिस्टम की लॉन्चिंग भी की।

मंत्री ने कहा कि झारखंड की शहरी आबादी अब नगर विकास विभाग से जुड़ी समस्याओं का पीजीएमएस पोर्टल में ऑनलाइन शिकायत कर समाधान पा सकती है। लोग बिल्डिंग प्लान एप्रूवल के लिए ऑनलाइन आवेदन दे सकते हैं। साथ ही भूगतान भी ऑनलाइन कर सकते हैं, जो फारदर्शी होगा। इससे शिकायत नहीं रहेगी।



प्रोजेक्ट बिल्डिंग में तीन पॉलिसियों का विमोचन, वो पोर्टल का हुआ शुभारंभ।

### सिंगल विंडो सिस्टम लागू होने से परेशानी दूर होगी

मंत्री सिंह ने कहा, सरकार का प्रयास है कि राज्य में रहने वाले सभी लोगों का अपना पक्का मकान हो। सरकार फ्लाइओवर, हटयू लकी जैसे सभी मामलों का समाधान करने का प्रयास कर रही है। सिंगल विंडो सिस्टम लागू हो, जिससे लोगों को कई बजटों के चक्कर न लगाने पड़े।

### इनका हुआ विमोचन

- झारखंड अफोर्डेबल अर्बन हाउसिंग पॉलिसी • झारखंड वाटर यूजर चार्जिंग पॉलिसी फॉर अर्बन एरिया • एडवर्टीजमेंट पॉलिसी फॉर अर्बन लोकल बॉडीज

इन नंबरों पर कर सकते हैं शिकायत : कॉल सेंटर व हेल्पलाइन नंबर 0651-7122727, 7633928444 पर सोमवार से शनिवार, समय 10 बजे से शाम 5 बजे तक, एक्सप्रेस तथा वॉटरसप नं. 7633928444 में • पीजीएमएस@डीएमआरखंड.इन

**LAUNCH OF PGMS PORTAL**

Directorate Of Municipal Administration  
Government Of Jharkhand

Honorable Prime Minister Of India  
**Shri Narendra Modi**

Honorable Chief Minister Of Jharkhand  
**Shri Raghuraj Das**

Honorable Minister of Urban Development, Housing & Transport Department, Jharkhand  
**Shri C.P. Singh**

Directorate Of Municipal Administration, 3rd Floor FFP Building, Dumas  
Ranchi-834004, Jharkhand  
info@dmajharkhand.in www.dmajharkhand.in

### How to Lodge a Complaint Public Grievances Management System (PGMS)

- Call Center 065-1712-2727
- Website [www.dmajharkhand.in](http://www.dmajharkhand.in)
- SMS 763-392-8444
- Mail [pgms@dmajharkhand.in](mailto:pgms@dmajharkhand.in)
- WhatsApp 763-392-8444
- Mobile App Coming soon

**Helpline 065-1712-2727**



**We are always Ready to help you!**  
**Monday to Saturday**  
 10 AM to 5 PM



# Jharkhand Affordable Urban Housing Policy



प्रभात खबर

सिटी फर्स्ट

शुरुआत. नगर विकास मंत्री ने जारी की शहरी आवास, वाटर यूजर चार्ज व विज्ञापन नीति

## लागत मूल्य पर सबको मिलेगा आवास

झारखंड सरकार सभी को लागत मूल्य पर आवास देगी, लेकिन इसका लाभ उन्हीं को मिलेगा, जिनके अपने या परिवार के किसी सदस्य के नाम से देश के किसी हिस्से में मकान न हो। आवास छह लाख रुपये तक के रहना आय वालों को ही मिलेगा। यह घोषणा राज्य सरकार की आवास नीति में की गयी है, जिसे नगर विकास मंत्री सीपी सिंह ने सोमवार को जारी किया है।

वर्तन संकायिका > टॉपी

नगर विकास मंत्री सीपी सिंह ने सोमवार को नगर विकास एवं आवास विभाग की तीन बैठकों जारी कीं। उनमें आवास नीति, वाटर यूजर चार्ज नीति और विज्ञापन नीति शामिल हैं। साथ ही कंजुमर विधायन विज्ञापन साइट, ऑनलाइन नक्शा और जुड़को की वेबसाइट भी लॉन्च की गयीं।

निदान : नीतियों के जारी करने के मौके पर नगर विकास मंत्री सीपी सिंह ने कहा कि विभाग जनता को हर समस्या के निदान के लिए तैयार है। पहली बार जनता की शिक्षा के लिए वेबसाइट भी तैयार की गयी है। ऑनलाइन नक्शा से पारदर्शिता आयेगी, उन्हीं कहा कि यह मंत्री होते हुए भी जनता को समस्या को देखते हैं। उन्हीं कहा कि सरकार सबको आवास देने के लिए प्रतिबद्ध है।

जल्द जारी की जायेगी एआईओएट की नीति : नगर विकास विभाग के प्रधान सचिव अरुण सिंह ने कहा कि एआईओएट की नीति शीघ्र जारी की जायेगी, इस बार शीघ्र अगस्त होये। राईट भवन की नीति जारी कर दी गयी है, उन्हीं कहा कि विकास में सरकार को कर्मों है उसे दूर किया जायेगा, स्वतंत्र भाषण युवा विद्वान राहुल शर्मा ने विकास और अपवाह प्रश्न आर सचिव राहुल कुमार ने किया। मौके पर आवास चार्ज के पारदर्शी आयोग गठित करने अरु अधिकारी मौजूद थे।

### बेघरों को मिलेगा अपना आशियाना

- कंजुमर विधायन रिड्रेसल साइट ऑनलाइन नक्शा और जुड़को की वेबसाइट भी लॉन्च की गयी
- उपभोक्ता अब ऑनलाइन दर्ज करा सकेगी शिक्षा चार्ज नवयौं के लिए आवेदन भी ऑनलाइन लिये जायेगे



1200 रुपये प्रति वर्ग फीट की दर से मिलेगा आवास

### दूसरी नीति : रिंग रोड में बड़ी होर्डिंग नहीं लगेगी

विभाग द्वारा एआईओएट की नीति पर अगस्त लोक बौद्धिक झारखंड-2016 जारी की गयी है। इसमें निकाय क्षेत्र के रिंग रोड व पैसी सड़कें, जहां परकीलेट कर खतर हो, वहां होर्डिंग नहीं लगेगी। पैडी व एंटी-सिस्टम स्थलों पर भी होर्डिंग नहीं लगेगी। निच निचको की अनुमति के लिए विज्ञापन नीति लम्बे जा सकेगी, एंटी-सिस्टम को निचको में मिश्रित करना होगा। निचको जगह के रिहायश से दूर रख करेगा।

### तीसरी नीति : पानी की खपत के अनुसार बिल

विभाग द्वारा झारखंड वाटर यूजर चार्ज की नीति 2016 पर अगस्त पुरिच जारी की गयी है। इसके अलावा उपभोक्ता विज्ञापन नीति की खपत करने आने की भी विन देते। उपभोक्ताओं के घरों में वाटर मीटर लगाने जायेगी, खपत के आधार पर पानी की टैरिफ की निश्चित की जायेगी। स्वतंत्र बस्तियों में भी वाटरपायपन से आगुंति सुनिश्चित की जायेगी।

### दो तरह के आवास बनायेगी सरकार

रोजाना के तहत सरकार दो तरह के आवास बनायेगी, पहला इकट्ठेपूर, यह उनके के लिए होगा, जिन्की सलाना आय तीन लाख रुपये तक है। दूसरा एलएचआई, यह उनके लिए होगा, जिन्की आय सलाना छह लाख रुपये तक है। आवास बनाने के लिए सरकार लैंड बैंक भी बनायेगी, जहां प्राइवेट सेक्टर के साथ मिल कर आवास का निर्माण किया जायेगा। इसके अलावा स्वतंत्र बस्तियों को दुरुस्त कर वहां रहनेवाले लोगों को आवास दिया जायेगा, सरकार को-ऑपरेटिव व टेलर पद्धति से भी आवास देगी।

होना झारखंड हाउसिंग मिलान का गठन : सरकार झारखंड हाउसिंग मिशन का गठन भी करेगी, जो-नीतियों को लागू करने के लिए विन-निर्देश जारी करेगा। इसके लिए एक स्वायत्त समिती बनायी गयी है। इसके अध्यक्ष मुख्यमंत्री होंगे। इसके अध्यक्ष नगर विकास मंत्री, भू-राजस्व मंत्री होंगे। साथ ही मुख्य सचिव, विकास अरुण, विल सचिव, भू-राजस्व सचिव व नगर विकास सचिव सदस्य होंगे। आवास की मंजूरी देने व मॉनिटरिंग के लिए मुख्य सचिव की अध्यक्ष में समिती गठित की जायेगी।

### अब कॉल सेंटर और ऑनलाइन शिकायत पोर्टल भी

विभाग द्वारा सोमवार को पब्लिक विनाय मेनेजमेंट पोर्टल भी जारी किया गया, जहां निचको से संबंधित शिकायत व सुझाव दिये जा सकेंगे हैं। कॉल सेंटर भी शुरू किया है। जिसका नंबर है 0651 7122777, 7633928444। मेमब्रांड नंबर सेवक या क्लर संपर्क कर भी शिकायत की जा सकती है। शिकायत नगर विकास की वेबसाइट पीएचएसएस डॉट ऑर झारखंड डॉट इन पर भी की जा सकती है।

### नक्शा के लिए आवेदन ऑनलाइन लिया जायेगा

विभाग द्वारा सभी निचको में नक्शा का आवेदन ऑनलाइन लिया जायेगा। इसे ऑनलाइन ही पुरिच किया जायेगा। विभाग द्वारा ऑनलाइन बिक्रीका अद्यतन मेनेजमेंट सिस्टम बनाया गया है। जहां अलग-अलग निचको के लिए ऑनलाइन आवेदन दिये जा सकेंगे। विभाग द्वारा झारखंड अरुण डेवलपमेंट रेगुलेशन कोड (जुड़को) की वेबसाइट भी लॉन्च की गयी।

## बिहार और झारखंड : अफोर्डेबल हाउसिंग पॉलिसी, हर गांव में सड़क

झारखंड में 2017-18 में सड़क निर्माण के लिए 5464 करोड़ का बजट है। 2821 करोड़ रुपए ग्रामीण क्षेत्रों में सड़क निर्माण पर खर्च किए जाएंगे। 2019 तक 20 हजार किलोमीटर ग्रामीण सड़क बनाने का लक्ष्य निर्धारित है। इसके अलावा 2 हजार करोड़ रुपए भवन निर्माण के लिए आवंटित किए गए हैं। राज्य सरकार ने क्रिप्रायती आवास नीति बनाई है, जिसके अंतर्गत बिल्डर्स को कम ब्याज पर लोन की सुविधा मिलेगी। वहीं, बिहार में सरकार ने हर गांव में सड़क पहुंचाने का लक्ष्य तय किया है। इसके लिए ब्रिक्स बैंक से लोन लेने की तैयारी है। सरकार ने रोड विजन 2020 को मंजूरी दी है, जिसका मकसद राज्य में रोड नेटवर्क को बेहतर बनाना है। इधर, हाउसिंग को बढ़ावा देने के लिए पब्लिक-प्राइवेट पार्टनरशिप मॉडल को बढ़ावा दिया जा रहा है।



# 16 को मिला आशियाना, खिल उठे चेहरे

जागरण संवाददाता, जमशेदपुर: काठ जगर्ण सह संसदीय कार्यमंत्री सरजू वरु व जमशेदपुर के सांसद विद्युत वरुण महांती ने शनिवार को बलौंदुब के चिखरीदुर्ग में पीएम आवास योजना के तहत बनाए गए पहले एक इन्फोस्टेशन किया। 16 फीट में लानुकों ने प्रवेश किया। मंत्री व सांसद ने हर घर में जकार लानुकों से बात की। जिनका मूड प्रवेश हुआ उनके परिवारों के चेहरे खिले हुए थे। इस दौरान सरजू वरु ने कहा कि प्रधानमंत्री नरेद्र मोदी के सपने अब धरतल पर उतरे दिख रहे हैं। उन्होंने कहा कि लानुका अपने मकान में और जैसा चाहें वैसा निर्माण कर सकते हैं। सांसद विद्युत वरुण महांती ने कहा कि जनप्रतिनिधियों के साथ ही अक्षेप के पदाधिकारियों ने ईमानदारी से काम किया। इसका परिणाम यह हुआ कि चेरलान के पहले पीएम आवास योजना के लानु बने पहले में लोग खड़े लगे हैं। बच्चों अक्षेप के विशेष पदाधिकारी जमशेदपुर प्रसाद खरन ने कहा कि इस योजना के तहत जैसे-जैसे मकान बने जायेंगे, वैसे-वैसे मकान लानुकों को जलखंड होते जायेंगे। इस अवसर पर सजीव कुमर, चितरंजन वर्मा, विकास सिंह, संजया वंदे, रंजन रंजन, देवकीश प्रधान, निखरंज मिश्रा, भोलू चंडेव, अमोदि मिश्रा के अलावा बहुत संख्या में भाजपाई व स्थानीय लोग उपस्थित थे।



**पीएम आवास योजना का विवरण**

**कुल लानुका**  
**3 लाख 62100 रुपये**  
 सरकार द्वारा अनुदान  
**2 लाख 25 हजार**  
**लानुका को प्रथम चिखर**  
**45000 रुपये**  
 द्वितीय चिखर : 67500 रुपये  
 तृतीय चिखर : 45000 रुपये  
 चतुर्थ चिखर : 67500 रुपये  
**लानुका का अंशदान**  
**1 लाख 37100 रुपये**

**इन लानुकों को मिला मकान**

नाम	स्थान
अनुराग सोहन	बलौंदुब चिखरीदुर्ग
जयंत हासरा	बलौंदुब चिखरीदुर्ग
शिशु हांसरा	बलौंदुब चिखरीदुर्ग
सुखन काना	बलौंदुब इस्टेट
नरेंद्र सरने	बलौंदुब चिखरीदुर्ग
सोहन सोहन	बलौंदुब चिखरीदुर्ग
सोहनवामरुण	बलौंदुब चिखरीदुर्ग
शिलांजलि सोहन	बलौंदुब चिखरीदुर्ग
खेत मुं	बलौंदुब चिखरीदुर्ग
निखर पल्लीन	दुर्ग-डी.बो.बालू, अजयनगर
नौ. सोहन	लावाकनगर, अजयनगर
अक्षयज अरुण	दुर्ग-डी.बो.बालू, डी.न.बो.डी.
महाकुंड इरान	अजयनगर, मकान
शिता देवी	दुर्ग-जमशेदपुर, डी.बो.बालू
भयमनी देवी	दुर्ग-जमशेदपुर, मकान
कमल देवी	जेलर पुररुदुका रोड

**कुल मकान**  
 कुल स्वीकृत अंशदान - 563  
 निर्माण कार्य शुरू - 527  
 बीच टेंडर तक कार्य - 216  
 सिंटर लेकन तक कार्य - 46  
 आ तक का निर्माण - 39  
 पूर्णरूप से तैयार मकान - 16

**पीएम आवास योजना**

- संसदीय कार्य मंत्री के साथ सांसद ने किया उद्घाटन
- धरतल पर उतर रही प्रधानमंत्री की घोषणा : सरजू



# चिरकुंडा >> लाभुकों के बीच 29 लाख का ऋण वितरित



**चिरकुंडा.** बैंक ऑफ बड़ौदा चिरकुंडा शाखा द्वारा मंगलवार को नप कार्यालय में प्रधानमंत्री आवास योजना व मुद्रा योजना के लाभुकों के बीच 29 लाख रुपया ऋण के रूप में वितरित किया. कुल नौ लाभुकों के बीच चेक का वितरण नप के कार्यपालक पदाधिकारी अरुण कुमार व शाखा प्रबंधक नुपुर भारती ने किया. मौके पर सिटी मैनेजर विकास रंजन व ललित लकड़ा, पार्षद इरफान अहमद खान, बैंककर्मी व लाभुक उपस्थित थे.

# Financial Status of PMAY

Rs In Lakhs


Project Sanctioned in CSMC	DU's Approved	Fund Received from GOI	State Share released	Expenditure as on date	UC Sent
4 <sup>th</sup> and 6 <sup>th</sup> CSMC	Downsized sanctioned DU's 7739 (20239)	12143.40 (Fund @ 7739 is = 4643.40)	6071.7 (Fund @ 7739 is = 2321.70)	5355.90	5355.90 (Central =3575.42 + State=1780.48)
12th CSMC	19933	4459.80	2229.90	2516.30	00.00
14th CSMC	12814	7688.40	3844.20	2867.46	00.00
<b>Total</b>		<b>24291.60</b>	<b>12145.80</b>	<b>10738.66</b>	<b>5355.90</b>

# Housing Demand

Housing demand across four verticals for the 41 ULBs.

Total demand (Revised) till date

Slum Redevelopment through private participation	Credit Linked Subsidy	Affordable Housing in partnership	Beneficiaries led Construction	Total
89742	5481	37296	86389	218908



# Proposal of 37 BLC Projects

# HUDCO, Jharkhand Team visited Lohardagga & Dhanbad to review proposed DPR DPR submitted to GOI – Madhupur

					
Name	(WARD NO.)	Beneficiary ID No.	Name	(WARD NO.)	Beneficiary ID No.
Sanju Kumari	19	255301000005495	Amrita Devi	19	255301000003015

					
Name	(WARD NO.)	Beneficiary ID No.	Name	(WARD NO.)	Beneficiary ID No.
Ganpati Mahto	20	342604549522	Kamal Oraon	20	760458384339



# Dwelling Unit Cost

## Design & Dwelling Unit Cost approved from SLAC


<b>Total Carpet area</b>	<b>28.42 sq mt.</b>
<b>Total Cost</b>	<b>3.621 lakhs</b>



## Beneficiaries led individual construction

<b>GOI Contribution</b>	<b>1.50 Lakhs</b>
<b>State Contribution</b>	<b>0.75 Lakhs</b>
<b>Beneficiary Contribution</b>	<b>1.371 Lakhs</b>
<b>Total Cost</b>	<b>3.621 Lakhs</b>

# Building plan for proposed DUs

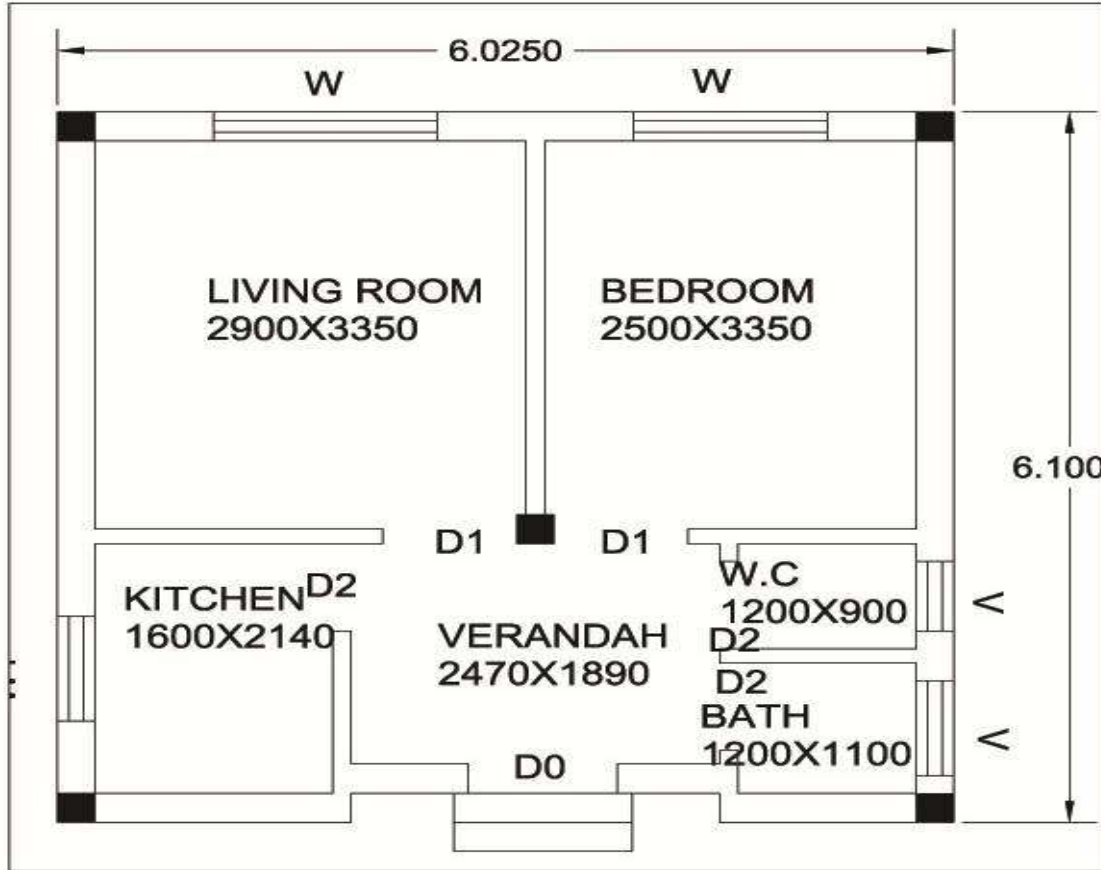

SCHEDULE OF DOOR & WINDOWS					
TYPE	WIDTH	HEIGHT	SILL	LINTEL	DESCRIPTION
D0	1.00	2.10	0	2.10	Single panelled door
D	0.90	2.10	0	2.10	Single panelled door
D1	0.75	2.10	0	2.10	Single panelled pvc door
D2	0.60	2.10	0	2.10	Single panelled pvc door
W	1.50	1.20	0.90	2.10	Glazed steel window
W1	0.90	1.20	0.90	2.10	Glazed steel window
V	0.60	0.75	1.50	2.10	Glazed steel

ALL DIMENSION ARE IN METRE



## Abstract details of proposed projects (PMAY 16-17) (At Glance)

ULB	Proposed Beneficiaries for FY 16-17	Central Share @ Rs.1.5 Lakh	State Share @ Rs. 0.75 Lakh	Beneficiaries Contribution @ Rs. 1.371 Lakh	Total Cost of DUs	Unit Cost per DU
Total Cost	<b>20430</b>	<b>30645.00</b>	<b>15322.5</b>	<b>28009.53</b>	<b>73977.03</b>	<b>3.621</b>

# Abstract details of proposed projects

## DPR Summary Report for Individual Beneficiary-led Construction (Vertical IV) Under PMAY for Financial Year 2016-2017 Phase III Jharkhand.

Sl. No.	ULBs	Proposed Beneficiaries for FY 16-17	Central Share @ Rs.1.5 Lakh	State Share @ Rs. 0.75 Lakh	Beneficiaries Contribution @ Rs. 1.371 Lakh	Total Cost of DUs	Unit Cost of per DU
1	Basukinath	158	237.000	118.500	216.618	572.118	3.621
2	Bundu	293	439.500	219.750	401.703	1060.953	
3	Chaibasa	644	966.000	483.000	882.924	2331.924	
4	Chakradharpur	148	222.000	111.000	202.908	535.908	
5	Chakuliya	394	591.000	295.500	540.174	1426.674	
6	Chas	1249	1873.500	936.750	1712.379	4522.629	
7	Chatra	150	225.000	112.500	205.650	543.150	
8	Chirkunda	102	153.000	76.500	139.842	369.342	
9	Deoghar	2182	3273.000	1636.500	2991.522	7901.022	
10	Dhanbad	1905	2857.500	1428.750	2611.755	6898.005	
11	Dumka	56	84.000	42.000	76.776	202.776	
12	Garhwa	570	855.000	427.500	781.470	2063.970	
13	Giridih	413	619.500	309.750	566.223	1495.473	
14	Godda	449	673.500	336.750	615.579	1625.829	
15	Gumla	630	945.000	472.500	863.730	2281.230	
16	Hussainabad	409	613.500	306.750	560.739	1480.989	
17	Jamtara	386	579.000	289.500	529.206	1397.706	
18	Jhumri Telaiya	1313	1969.500	984.750	1800.123	4754.373	

**Cont.**

Sl. No.	ULBs	Proposed Beneficiaries for FY 16-17	Central Share @ Rs.1.5 Lakh	State Share @ Rs. 0.75 Lakh	Beneficiaries Contribution @ Rs. 1.371 Lakh	Total Cost of DUs	Unit Cost of per DU
19	Jugsalai	5	7.500	3.750	6.855	18.105	3.621
20	Khunti	530	795.000	397.500	726.630	1919.130	
21	Koderma	305	457.500	228.750	418.155	1104.405	
22	Latehar	450	675.000	337.500	616.950	1629.450	
23	Lohardaga	1099	1648.500	824.250	1506.729	3979.479	
24	Madhupur	1292	1938.000	969.000	1771.332	4678.332	
25	Majhiyaon	305	457.500	228.750	418.155	1104.405	
26	Mango (NAC)	19	28.500	14.250	26.049	68.799	
27	Medininagar	867	1300.500	650.250	1188.657	3139.407	
28	Mihijam	32	48.000	24.000	43.872	115.872	
29	Nagar Untari	16	24.000	12.000	21.936	57.936	
30	Pakur Nagar	331	496.500	248.250	453.801	1198.551	
31	Phusro Nagar	34	51.000	25.500	46.614	123.114	
32	Rajmahal Nagar	142	213.000	106.500	194.682	514.182	
33	Ramgarh	190	285.000	142.500	260.490	687.990	
34	Ranchi	2668	4002.000	2001.000	3657.828	9660.828	
35	Sahebganj	176	264.000	132.000	241.296	637.296	
36	Saraikele	9	13.500	6.750	12.339	32.589	
37	Simdega	509	763.500	381.750	697.839	1843.089	
Total		20430	30645.00	15322.5	28009.53	73977.03	3.621

## Abstract details of Categories of Beneficiaries

<b>ULBs</b>	<b>Total No. of beneficiaries</b>	<b>Gen</b>	<b>SC</b>	<b>ST</b>	<b>OBC</b>	<b>Total</b>	<b>Minority</b>	<b>Person with Disability</b>
<b>37</b>	<b>20430</b>	<b>2181</b>	<b>3478</b>	<b>2957</b>	<b>11814</b>	<b>20430</b>	<b>3743</b>	<b>20</b>

# Categories of Beneficiaries



PMAY 2016-17 Phase III			No. of beneficiaries covered in the Project							No. of houses to be construct /acquire, <i>Please specify ownership (any of these)</i>			
Sl.No.	ULB	Total No. of beneficiaries	Gen	SC	ST	OBC	Total	Minority	Person with Disability	Joint (01)	Female (02)	Male (03)	Trangender(04)
1	Basukinath	158	15	31	8	104	158	0	0	0	56	102	0
2	Bundu	293	55	19	64	155	293	14	2	0	210	83	0
3	Chaibasa	644	60	54	202	328	644	178	0	0	187	457	0
4	Chakradharpur	148	25	19	67	37	148	0	0	0	56	92	0
5	Chakuliya	394	40	30	57	267	394	67	0	0	174	220	0
6	Chas	1249	316	208	30	695	1249	230	0	0	776	473	0
7	Chatra	150	18	40	8	84	150	55	0	0	89	61	0
8	Chirkunda	102	13	54	0	35	102	17	1	0	59	43	0
9	Deoghar	2182	66	721	27	1368	2182	149	0	0	937	1245	0
10	Dhanbad	1905	242	337	88	1238	1905	213	0	0	921	984	0
11	Dumka	56	7	12	0	37	56	5	0	0	26	30	0
12	Garhwa	570	186	108	38	238	570	126	0	0	266	304	0
13	Giridih	413	28	48	0	337	413	143	0	0	228	185	0
14	Godda	449	50	20	11	368	449	193	5	0	256	193	0
15	Gumla	630	80	21	225	304	630	100	0	0	323	307	0
16	Hussainabad	409	81	162	0	166	409	109	3	0	234	175	0
17	Jamtara	386	14	109	9	254	386	49	0	0	170	216	0
18	Jhumri Telaiya	1313	169	277	35	832	1313	0	0	0	1035	278	0

# Cont..

			No. of beneficiaries covered in the Project							No. of houses to be construct /acquire, Please specify ownership (any of these)			
Sl.No.	ULB	Total No. of beneficiaries	Gen	SC	ST	OBC	Total	Minority	Person with Disability	Joint (01)	Female (02)	Male (03)	Trangender (04)
19	Jugsalai	5	1	3	0	1	5	0	0	0	2	3	0
20	Khunti	530	25	89	95	321	530	25	0	0	263	267	0
21	Koderma	305	39	88	16	162	305	62	7	0	226	79	0
22	Latehar	450	6	188	33	223	450	0	0	0	436	14	0
23	Lohardaga	1099	133	62	157	747	1099	328	0	0	665	434	0
24	Madhupur	1292	47	223	141	881	1292	518	0	0	489	803	0
25	Majhiyaon	305	33	93	1	178	305	27	0	0	299	6	0
26	Mango (NAC)	19	5	2	0	12	19	1	0	0	13	6	0
27	Medininagar	867	58	18	0	791	867	191	0	0	356	511	0
28	Mihijam	32	5	7	8	12	32	2	0	0	30	2	0
29	Nagar Untari	16	3	13	0	0	16	0	0	0	1	15	0
30	Pakur Nagar	331	24	94	43	170	331	0	0	0	158	173	0
31	Phusro Nagar	34	8	5	0	21	34	10	0	0	11	23	0
32	Rajmahal Nagar	142	1	14	0	127	142	61	2	0	80	62	0
33	Ramgarh	190	7	15	76	92	190	39	0	0	167	23	0
34	Ranchi	2668	250	182	1317	919	2668	385	0	0	1544	1124	0
35	Sahebganj	176	3	68	2	103	176	0	0	0	73	103	0
36	Saraikelela	9	5	0	0	4	9	0	0	0	0	9	0
37	Simdega	509	63	44	199	203	509	446	0	0	217	292	0
		<b>20430</b>	<b>2181</b>	<b>3478</b>	<b>2957</b>	<b>11814</b>	<b>20430</b>	<b>3743</b>	<b>20</b>	<b>0</b>	<b>11033</b>	<b>9397</b>	<b>0</b>

## **Initiative under vertical I**

- Total 400 slums identified in HFAPoA
- Land identified and verified at ULB level
- Draft DPRs are being prepared by JUIDCO / consultants
- RFP for redevelopment of slums under PPP mode will be finalized in two weeks.

## **Initiative under vertical III**

- RFP finalized for construction of 40000 DUs using new and emerging Technologies across the state under Hybrid Annuity Model.

## Issues/ Suggestions in MIS & BhuvanHFA App

- The beneficiaries are attached with respective DPR on PMAY-MIS, their name is not reflecting in bhuvan app immediately. It takes more than 3 days to be reflected in the mobile.
- In MIS application duplicate entry is still being accepted.
- During geo-tagging we cannot see the different stages of geo-tagged photograph in BhuvanHFA mobile app.

## Others

- Release of IInd Installment of Rs 4643.40 lakhs for 7739 (Downsized DUs)
- Inclusion of three more urban local bodies (Chatterpur, Kapali and Bharharwa) under PMAY.



# Work Progress under RAY



Sl. No.	ULBs	No. of Beneficiary As Per DPR	Work Completed	Work in Progress	% Work Completed	Non Starter	Dus to be drop
1	Chas	383	148	145	38.64	90	0
2	Dhanbad	1983	1099	297	55.42	0	587
3	Ranchi	1565	402	873	25.68	19	271
Total		3931	1649	1315	33.45	109	858

# RAY PROJECT, CHAS



# RAY PROJECT, CHAS



# RAY PROJECT, Ranchi



# Financial Status of BSUP/IHSDP/RAY

Project s	DU's Approved	Fund Received from GOI	State Share released	Expenditure as on date	UC Sent (In Lakh)
RAY	3931	5636.95	5998.24	8454.32	5823.63 (4000.00+1823.63)

☐ Requested to release IInd Installment of Rs 1823.63 lakhs under RAY

Thanks



# JnNURM Progress

JnNURM	DUs taken up	DUs completed	Percentage	DUs in Progress	Dropped DUs
BSUP	2490	2077	83.41	257	156
IHSDP	7593	6407	84.24	1124	62
Total	10083	8484	73.35	1381	218

# Work Progress under BSUP



Sl. No.	ULBs	No. of Beneficiary As Per DPR	DU's Drop	Work Completed	Work in Progress	% Work Completed
1	Ranchi	2458	150	2051	257	83.44
2	Dhanbad	32	6	26	0	81.25
Total		2490	156	2077	257	83.41



# Work Progress under IHSDP



Sl. No.	ULBs	No. of Beneficiary As Per DPR	Work Completed	Work in Progress	% Work Completed	Dus to be drop
1	Chaibasa	380	352	24	92.63	4
2	Chatra	897	828	57	92.31	12
3	Giridih	1132	1126	0	99.47	6
4	Gumla	863	777	74	90.03	12
5	Hazaribag	949	797	152	83.98	0
6	Lohardaga	1623	1540	83	94.89	0
7	Medninagar	420	418	0	99.52	2
8	Mihijam	816	304	505	37.25	7
9	Phusro	204	162	42	79.41	0
10	Seraikela	309	103	187	33.33	19
<b>Total</b>		<b>7593</b>	<b>6407</b>	<b>1124</b>	<b>84.38</b>	<b>62</b>

# Financial Status of BSUP/IHSDP/RAY

Project s	DU's Approved	Fund Received from GOI	State Share released	Expenditure as on date	UC Sent (In Lakh)
RAY	3931	5636.95	5998.24	8454.32	5823.63 (4000.00+1823.63)
IHSDP	7593	9706.05	8160.72	12636.17	9523.78
BSUP	2490	8218.03	6526.78	5208.66	3252.34
<b>Total</b>	<b>14014</b>	<b>23561.03</b>	<b>20685.74</b>	<b>26299.15</b>	<b>18599.80</b>

## PMAY 2015-16 Status Report

Sl. No.	ULBs	Target	Agreement	% Agreement	Work Started	% Work Started	Work Started out of total				
							Foundation	Plinth	Roof	Finishing	Total
1	Adityapur	374	374	100	374	100.00	154	138	57	25	374
2	Basukinath	64	64	100	64	100.00	5	29	22	8	64
3	Bishrampur	140	140	100	140	100.00	40	85	15	0	140
4	Bundu	98	92	94	92	93.88	9	14	58	11	92
5	Chaibasa	316	316	100	312	98.73	42	95	129	46	312
6	Chakardharpur	224	224	100	224	100.00	10	47	97	70	224
7	Chakulia	75	75	100	75	100.00	3	15	29	28	75
8	Chas	282	282	100	282	100.00	0	114	150	18	282
9	Chatra	70	70	100	70	100.00	0	68	2	0	70
10	Chirkunda	62	62	100	60	96.77	17	10	27	6	60
11	Deoghar	490	490	100	490	100.00	2	365	110	13	490
12	Dhanbad	539	537	100	533	98.89	42	292	161	38	533
13	Dumka	33	33	100	33	100.00	1	11	12	9	33
14	Garhwa	157	157	100	157	100.00	9	35	64	49	157
15	Giridih	362	362	100	362	100.00	220	136	6	0	362
16	Godda	206	206	100	206	100.00	0	0	156	50	206
17	Gumla	175	175	100	175	100.00	15	45	50	65	175
18	Hazaribag	447	421	94	421	94.18	279	93	41	8	421
19	Hussainabad	95	95	100	95	100.00	37	49	9	0	95
20	Jamtara	125	125	100	110	88.00	10	72	28	0	110
21	Jhumri Tilaiya	305	290	95	290	95.08	15	179	95	1	290
22	Khunti	121	121	100	121	100.00	19	63	39	0	121

Sl. No.	ULBs	Target	Agreement	% Agreement	Work Started	% Work Started					
							Foundation	Plinth	Roof	Finishing	Total
23	Kodarma	94	94	100	94	100.00	3	14	67	10	94
24	Latehar	112	112	100	112	100.00	1	30	67	14	112
25	Lohardaga	186	186	100	186	100.00	52	114	19	1	186
26	Madhupur	135	131	97	130	96.30	61	49	20	0	130
27	Mango	72	72	100	72	100.00	0	9	46	17	72
28	Manjhiaon	62	62	100	62	100.00	2	50	8	2	62
29	Medininagar	151	151	100	151	100.00	6	45	44	56	151
30	Mihijam	150	147	98	51	34.00	31	20	0	0	51
31	Nagar Uttari	21	21	100	21	100.00	0	14	6	1	21
32	Pakur	190	190	100	190	100.00	0	62	110	18	190
33	Phusro	105	105	100	89	84.76	6	5	60	18	89
34	Rajmahal	90	90	100	87	96.67	0	1	75	11	87
35	Ramgarh	165	165	100	162	98.18	5	6	144	7	162
36	Ranchi	884	883	100	833	94.23	667	139	27	0	833
37	Sahibganj	330	330	100	315	95.45	0	119	185	11	315
38	Seraikela	55	55	100	54	98.18	4	21	16	13	54
39	Simdega	177	177	100	177	100.00	6	52	69	50	177
<b>Total</b>		<b>7739</b>	<b>7682</b>	<b>99.26</b>	<b>7472</b>	<b>96.55</b>	<b>1773</b>	<b>2705</b>	<b>2320</b>	<b>674</b>	<b>7472</b>



## PMAY Status Report under vertical IV (2016-17) Phase I

Sl. No.	ULBs	Target	Agreement with beneficiaries	% Agreement with beneficiaries	Work Started	% Work Started	Work Started out of total				
							Foundation	Plinth	Roof	Finishing	Total
1	Adityapur Nagar Parishad	213	213	100.00	194	<b>91.08</b>	194	0	0	0	194
2	Basukinath Nagar Panchayat	309	309	100.00	309	<b>100.00</b>	269	40	0	0	309
3	Bishrampur Nagar Panchayat	609	590	96.88	305	<b>50.08</b>	305	0	0	0	305
4	Bundu Nagar Panchayat	224	183	81.70	141	<b>62.95</b>	118	17	4	2	141
5	Chaibasa Nagar Parishad	537	529	98.51	307	<b>57.17</b>	279	28	0	0	307
6	Chakradharpur Nagar Parishad	413	413	100.00	311	<b>75.30</b>	185	101	25	0	311
7	Chakuliya Nagar Panchayt	448	440	98.21	292	<b>65.18</b>	251	38	2	1	292
8	Chatra Nagar Parishad	122	121	99.18	76	<b>62.30</b>	55	21	0	0	76
9	Chirkunda Nagar Parishad	65	65	100.00	56	<b>86.15</b>	7	34	15	0	56
10	Deoghar Municipal Corporation	1725	1725	100.00	1415	<b>82.03</b>	960	451	4	0	1415
11	Dumka Nagar Parishad	59	59	100.00	59	<b>100.00</b>	26	27	6	0	59
12	Garhwa Nagar Parishad	892	840	94.17	840	<b>94.17</b>	579	229	32	0	840
13	Giridih nagar Parishad	718	718	100.00	698	<b>97.21</b>	506	186	6	0	698
14	Godda Nagar Parishad	464	464	100.00	464	<b>100.00</b>	22	295	147	0	464
15	Gumla Nagar Parishad	491	488	99.39	402	<b>81.87</b>	326	66	10	0	402
16	Hazaribagh Nagar	1477	1341	90.79	951	<b>64.39</b>	951	0	0	0	951

Sl. No.	ULBs	Target	Agreement with beneficiaries	% Agreement with beneficiaries	Work Started	% Work Started	Work Started out of total				
							Foundation	Plinth	Roof	Finishing	Total
17	Hussainabad Nagar Panchayat	89	89	100.00	89	100.00	56	33	0	0	89
18	Jamtara Nagar Parishad	544	544	100.00	260	47.79	260	0	0	0	260
19	Jhumri Telaiya Nagar Parishad	821	761	92.69	388	47.26	369	19	0	0	388
20	Jugsalai Nagar Parishad	9	8	88.89	6	66.67	4	2	0	0	6
21	Khunti Nagar Panchayat	431	403	93.50	268	62.18	238	18	12	0	268
22	Koderma Nagar Panchayat	265	255	96.23	166	62.64	166	0	0	0	166
23	Latehar Nagar Panchayat	472	472	100.00	385	81.57	385	0	0	0	385
24	Madhupur Nagar Panchayat	292	281	96.23	163	55.82	109	36	18	0	163
25	Majhiyaon Nagar Panchayat	806	753	93.42	365	45.29	365	0	0	0	365
26	Medininagar Nagar Parishad	496	476	95.97	249	50.20	200	49	0	0	249
27	Nagar Utari Nagar Panchayat	37	37	100.00	37	100.00	18	17	2	0	37
28	Pakur Nagar Parishad	249	240	96.39	201	80.72	201	0	0	0	201
29	Rajmahal Nagar Panchayat	387	387	100.00	351	90.70	350	1	0	0	351
30	Ranchi Municipal Corporation	5101	4950	97.04	3319	65.07	3241	62	16	0	3319
31	Sahebganj Nagar Parishad	356	345	96.91	295	82.87	295	0	0	0	295
32	Saraikeela Nagar Parishad	91	90	98.90	90	98.90	90	0	0	0	90
33	Simdega Nagar Panchayat	721	721	100.00	721	100.00	516	180	25	0	721
<b>Total</b>		<b>19933</b>	<b>19310</b>	<b>96.87</b>	<b>14173</b>	<b>71.10</b>	<b>11896</b>	<b>1950</b>	<b>324</b>	<b>3</b>	<b>14173</b>

**PMAY Status Report under vertical IV (2016-17) Phase II**

Sl. No.	ULBs	Target	Agreement with beneficiaries	% Agreement with beneficiaries	Work Started	% Work Started	Work Started out of total				
							Foundation	Plinth	Roof	Finishing	Total
1	Adityapur Nagar Parishad	482	482	100.00	377	<b>78.22</b>	377	0	0	0	377
2	Basukinath Nagar Panchayat	19	19	100.00	19	<b>100.00</b>	19	0	0	0	19
3	Bishrampur Nagar Panchayat	38	38	100.00	38	<b>100.00</b>	38	0	0	0	38
4	Bundu Nagar Panchayat	4	4	100.00	4	<b>100.00</b>	1	1	1	1	4
5	Chakradharpur Nagar Parishad	40	40	100.00	33	<b>82.50</b>	4	11	18		33
6	Chakuliya Nagar Panchayt	8	8	100.00	8	<b>100.00</b>	1	4	2	1	8
7	Chas nagar Nigam	2237	2230	99.69	1602	<b>71.61</b>	1459	143	0	0	1602
8	Chatra Nagar Parishad	123	121	98.37	91	<b>73.98</b>	70	21	0	0	91
9	Chirkunda Nagar Parishad	138	138	100.00	105	<b>76.09</b>	23	12	60	10	105
10	Deoghar Municipal Corporation	356	356	100.00	356	<b>100.00</b>	35	285	32	4	356
11	Dhanbad Municipal Corporation	1050	1050	100.00	1032	<b>98.29</b>	706	326	0	0	1032
12	Dumka Nagar Parishad	174	174	100.00	174	<b>100.00</b>	37	123	14	0	174
13	Garhwa Nagar Parishad	43	42	97.67	42	<b>97.67</b>	8	18	12	4	42
14	Giridih nagar Parishad	92	92	100.00	90	<b>97.83</b>	83	7	0	0	90
15	Gumla Nagar Panchayat	49	49	100.00	47	<b>95.92</b>	15	23	6	3	47
16	Hazaribagh Nagar Nigam	158	147	93.04	144	<b>91.14</b>	144	0	0	0	144
17	Hussainabad Nagar Panchayat	16	16	100.00	16	<b>100.00</b>	7	9	0	0	16
18	Jamtara Nagar Parishad	7	7	100.00	6	<b>85.71</b>	6	0	0	0	6
19	Jhumri Telaiya Nagar Parishad	47	47	100.00	45	<b>95.74</b>	3	20	22	0	45
20	Khunti Nagar Panchayat	47	45	95.74	45	<b>95.74</b>	11	25	9	0	45

Sl. No.	ULBs	Target	Agreement with beneficiaries	% Agreement with beneficiaries	Work Started	% Work Started	Work Started out of total				
							Foundation	Plinth	Roof	Finishing	Total
21	Koderma Nagar Panchayat	6	6	100.00	6	<b>100.00</b>	6	0	0	0	6
22	Latehar Nagar Panchayat	10	10	100.00	9	<b>90.00</b>	9	0	0	0	9
23	Lohardaga Nagar Parishad	1911	1799	94.14	1152	<b>60.28</b>	1140	12	0	0	1152
24	Madhupur Nagar Panchayat	90	90	100.00	81	<b>90.00</b>	54	12	15	0	81
25	Majhiyaon Nagar Panchayat	19	19	100.00	17	<b>89.47</b>	0	17	0	0	17
26	Mango (NAC)	491	455	92.67	455	<b>92.67</b>	180	223	45	7	455
27	Medininagar Nagar Parishad	167	167	100.00	167	<b>100.00</b>	15	40	50	62	167
28	Mihijam Nagar Panchayat	111	76	68.47	10	<b>9.01</b>	10	0	0	0	10
29	Pakur Nagar Parishad	25	25	100.00	25	<b>100.00</b>	19	6	0	0	25
30	Phusro Nagar Parishad	100	100	100.00	96	<b>96.00</b>	6	7	74	9	96
31	Rajmahal Nagar Panchayat	15	15	100.00	15	<b>100.00</b>	0	10	5	0	15
32	Ramgarh Cantonment Board	759	756	99.60	587	<b>77.34</b>	587	0	0	0	587
33	Ranchi Municipal Corporation	3893	3740	96.07	2362	<b>60.67</b>	2223	117	22	0	2362
34	Sahebganj Nagar Parishad	63	63	100.00	57	<b>90.48</b>	17	40	0	0	57
35	Saraikela Nagar Parishad	13	13	100.00	13	<b>100.00</b>	13	0	0	0	13
36	Simdega Nagar Panchayat	13	13	100.00	13	<b>100.00</b>	0	5	8	0	13
<b>Total</b>		<b>12814</b>	<b>12452</b>	<b>97.17</b>	<b>9339</b>	<b>72.88</b>	<b>7326</b>	<b>1517</b>	<b>395</b>	<b>101</b>	<b>9339</b>

