



प्रधान मंत्री  
आवास योजना-शहरी  
Pradhan Mantri Awas Yojana-Urban

*50<sup>th</sup> Meeting of the  
Central Sanctioning cum  
Monitoring  
Committee(CSMC)  
under  
Pradhan Mantri Awas  
Yojana - Housing For All*

*27<sup>th</sup> December, 2019*




**Urban Development & Housing Department  
Government of Madhya Pradesh**



# Madhya Pradesh: Urban Profile

Total Population	7.25 Crore
Total Urban Population	2.01 Crore
Percentage of Urban Population	27.58 %
No. of Urban Local Bodies (ULBs)	378
Municipal Corporations	16
Municipal Councils	98
Nagar Parishads	264

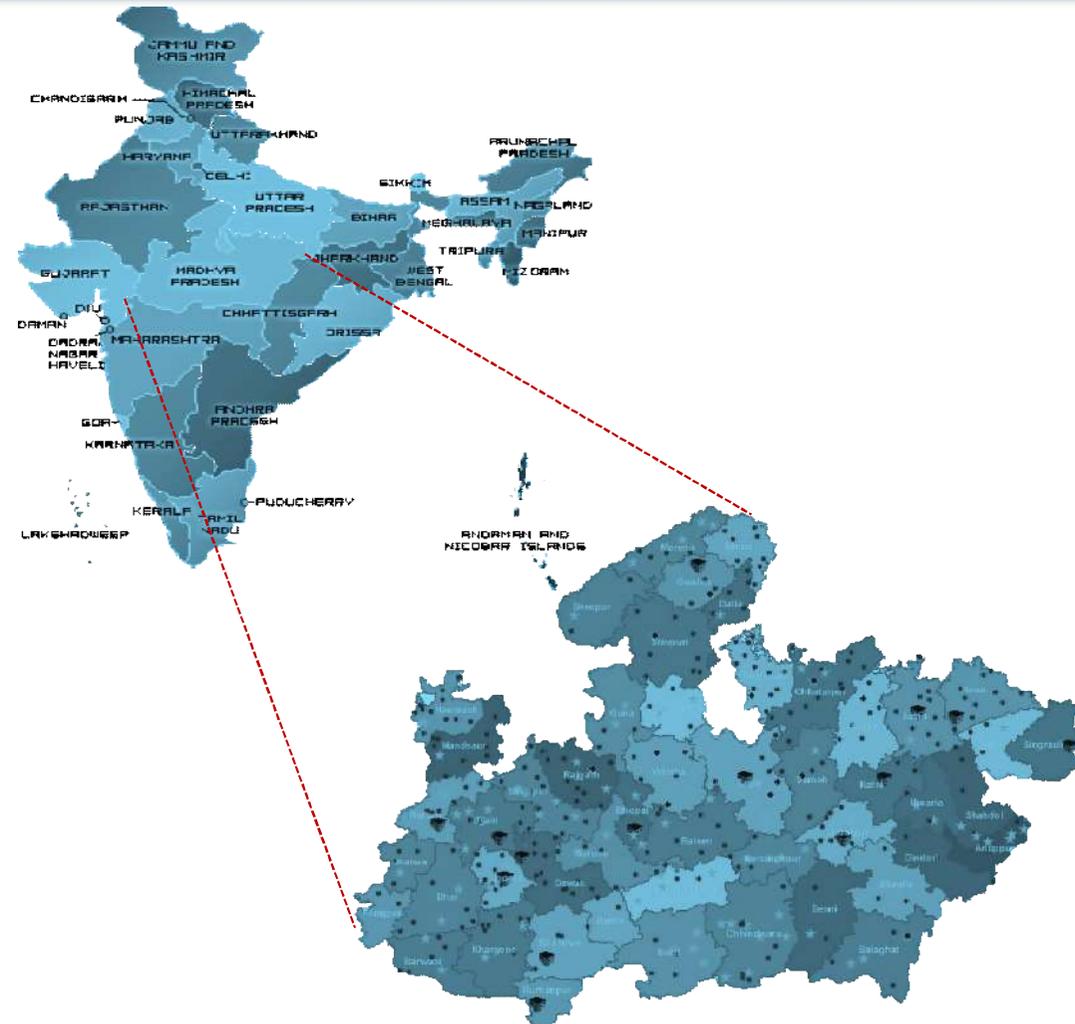

# Housing For All ó Funding Pattern

S. No.	Option	Central Government Initiative	State Government Share	Type of Beneficiary
1	"In-Situ" Slum Redevelopment (ISSR) with participation of private developers using land as a resource	Subsidy of amount of INR 1 lakh	<b>Free of Cost Land</b>	EWS
2	Affordable Housing through Credit Linked Subsidy Scheme (CLSS)	Interest Subsidy of upto 6.5/4/3 % on loan upto INR 6/9/12 lakhs for 20 years	-	EWS & LIG / MIG-1 / MIG-2
3	Affordable Housing in Partnership (AHP) with Public & Private sectors	Subsidy of amount of INR 1.5 lakh	<b>Subsidy of amount of INR 1.50 lakh for Slum Dwellers</b>	EWS
4	Subsidy for Beneficiary-Led Individual House Construction (BLC)	Subsidy of amount of INR 1.5 lakh	<b>Subsidy of amount of INR 1 lakh</b>	EWS

# Progress of PMAY(U)

Indicators	Current Status (No.)
▪ Cities Approved	378
▪ Demand Survey Completed	378
▪ Total Demand	11.52 Lakh
▪ Status of Survey Entry	10,56,791 Survey Data entered by ULBs
▪ Demand received through Common Service Centre and Online Application	4,53,149
▪ Cases accepted/rejected	2,15,373
▪ Whether HFAPoA Submitted	Yes, For all 378 Towns
▪ Whether AIP Submitted	Yes
▪ SLTC/CLTC staffs approved vs. placed	SLTC:10 vs 10 / CLTC: 449 vs 521
▪ Target of DUs in 2019-20	Sanctioning: 9.00 Lakh DUs Completion: 3.00 Lakh DUs
▪ State Budgetary Provision for PMAY (U) in 2019-20	As per provision of GoI matching budgetary provisions is ensured in state budget

# Interface with MIS

<b>Indicators</b>	<b>Current Status (No.)</b>
▪Projects approved:	1,423
▪Projects entered (7A/B/C/D)	1,423
▪DUs approved under BLC	5,69,349
▪Beneficiaries attached	4,99,541
▪Beneficiary Attachment Made (%)	87.74%
▪Geo-tagged Points	13,34,114 <i>(No. of Unique Houses Geo-Tagged: 4,01,312)</i>

# Details of Approved Projects

Vertical of the Scheme	No. of Cities/ Projects	No. of Dwelling Units				
		EWS	LIG	MIG-I	MIG-II	Total
Affordable Housing in Partnership (AHP)	47/76	1,42,080	48,708	18,150	88	<b>2,09,026</b>
Beneficiary Led Construction (BLC)	374/1343	5,69,349	-	-	-	<b>5,69,349</b>
In-Situ Slum Redevelopment (ISSR)	3/4	2,172	-	-	-	<b>2,172</b>
<b>Sub-Total Projects Approved by GoI:</b>	<b>378/1423</b>	<b>7,13,601</b>	<b>48,708</b>	<b>18,150</b>	<b>88</b>	<b>7,80,547</b>
Credit Linked Subsidy Scheme (CLSS)	-	15,478	20,949	7,407	758	<b>44,592</b>
<b>Total:</b>	<b>378/1,423</b>	<b>7,29,079</b>	<b>69,657</b>	<b>25,557</b>	<b>846</b>	<b>8,25,139</b>

# Physical Progress of Approved Projects as per MPR

Verticals	Approved DUs	In-Progress				Completed
		Foundation / Plinth	Lintel	Roof	Total	
AHP <i>(Excluding 66,946 LIG/MIG DUs)</i>	1,43,104	10,694	4,664	17,328	32,686	16,144
BLC (N)	5,69,436	66,801	32,074	27,455	1,26,330	2,15,540
ISSR	2,172	-	-	-	-	-
<b>Sub-Total of Approved Projects:</b>	<b>7,14,712</b>	<b>77,495</b>	<b>36,738</b>	<b>44,783</b>	<b>1,59,016</b>	<b>2,31,684</b>
CLSS <i>(Including LIG/MIG DUs)</i>	<b>47,209</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>47,209</b>
<b>Total:</b>	<b>7,61,921</b>	<b>77,495</b>	<b>36,738</b>	<b>44,783</b>	<b>1,59,016</b>	<b>2,78,893</b>

## Agenda:

# Approval of Detailed Project Reports (DPRs) under BLC Vertical

*Rs. in Crore*

<b>SLAC Date</b>	<b>No of Towns / Projects</b>	<b>No. of EWS DUs</b>	<b>Project Cost</b>	<b>Central Share</b>	<b>State Share</b>	<b>ULB Share</b>	<b>EWS Beneficiary Share</b>
16 <sup>th</sup> December 2019	32	13,276	510.5352	199.140	132.76	-	178.6352

# Project Proposal Brief

(Amount Rs. in Crore)

Verticals	ISSR	AHP	BLC (New)	BLC (E)	Remarks
▪No. of Projects	-	-	32	-	-
▪No. of DUs	-	-	13,276	-	-
▪Project Cost	-	-	510.5352	-	-
▪Central Share	-	-	199.140	-	-
▪State Share	-	-	132.76	-	-
▪ULB/ Implementing agency Share	-	-	-	-	-
▪Beneficiary Share	-	-	178.6352	-	-
▪PPP / LIG / MIG / HIG / Commercial	-	-	-	-	-

(Amount Rs. in Lakh)

Verticals	Per Unit Cost	Central Share	State Share	ULB/ Implementing agency Share	Beneficiary Share	Completion Time
▪BLC (N)	3.85	1.50	1.00	For Infrastructure	1.35	12/18 months from the date of work commencement

## City-Wise Details of DPR under Approval ó BLC

*Rs. in Crore*

S. No.	Name of City	No. of EWS DUs	Project Cost	Central Share	State Share	EWS Beneficiary Share
1	Agar	98	3.7689	1.470	0.98	1.3189
2	Amarpatan	278	10.6913	4.170	2.78	3.7413
3	Badoda-Sheopur	308	11.8580	4.620	3.08	4.1580
4	Barghat	80	3.0766	1.200	0.80	1.0766
5	Buxwaha	35	1.3460	0.525	0.35	0.4710
6	Chandia	1,110	42.7350	16.650	11.10	14.9850
7	Dhamnood-Ratlam	22	0.8461	0.330	0.22	0.2961
8	Dharampuri	995	38.3075	14.925	9.95	13.4325
9	Gairatganj	791	30.4203	11.865	7.91	10.6453
10	Garhakota	737	28.3435	11.055	7.37	9.9185
11	Gotegaon	414	15.9216	6.210	4.14	5.5716
12	Hatod	311	11.9735	4.665	3.11	4.1985
13	Jhabua	108	4.1535	1.620	1.08	1.4535
14	Khandwa	608	23.3988	9.120	6.08	8.1988
15	Khetia	305	11.7297	4.575	3.05	4.1047
16	Kothri-Sehore	250	9.6145	3.750	2.50	3.3645

## City-Wise Details of DPR under Approval ó BLC

*Rs. in Crore*

S. No.	Name of City	No. of EWS DUs	Project Cost	Central Share	State Share	EWS Beneficiary Share
17	Kumbhraj	622	23.9470	9.330	6.22	8.3970
18	Luvkush Nagar	255	9.8068	3.825	2.55	3.4318
19	Maihar	2,062	79.3870	30.930	20.62	27.8370
20	Mandla	117	4.4996	1.755	1.17	1.5746
21	Mungaoli	162	5.9454	2.430	1.62	1.8954
22	Niwari	193	7.4224	2.895	1.93	2.5974
23	Panagar	178	6.8455	2.670	1.78	2.3955
24	Piploda	105	4.0381	1.575	1.05	1.4131
25	Raghogarh-Vijaypur	956	36.7658	14.340	9.56	12.8658
26	Rehti	163	6.2687	2.445	1.63	2.1937
27	Rewa	300	11.5374	4.500	3.00	4.0374
28	Sendhwa-Barwani	302	11.6224	4.530	3.02	4.0724
29	Seoni	121	4.6534	1.815	1.21	1.6284
30	Shahpura-Dindori	575	22.1134	8.625	5.75	7.7384
31	Sihora	490	18.8444	7.350	4.90	6.5944
32	Susner	225	8.6531	3.375	2.25	3.0281
<b>Total:</b>		<b>13,276</b>	<b>510.5352</b>	<b>199.140</b>	<b>132.76</b>	<b>178,6352</b>



# Angikaar Campaign in Madhya Pradesh



# Progress of Angikaar Campaign

S. No.	Indicator	Current Status
1	Number of ARPs Registered	4,527
2	No. of Beneficiaries Targeted for Need Assessment	2,95,787
3	Need Assessment Done	2,52,000 (85%)
4	No. of Events Conducted	3,093
5	No. of Beneficiaries Covered through Door to Door Events	1,44,545
6	No. of Beneficiaries Attended City/Ward Level Events	4,48,537

# Financial Literacy Campaign

Indore



Bhopal

# Financial Literacy Campaign

Chhindwara



Indore

# State Level Workshop of Credit Linked Subsidy Scheme (CLSS)



# Promotion of Credit Linked Subsidy Scheme (CLSS)

Better Performing PLIs Awarded by State



State Level Workshop of CLSS

Promotion of CLSS in Indore

# Photographs

## Affordable Housing in Partnership (AHP)



## Progress of Approved AHP Projects



Site Visit of Jabalpur & Gwalior by PS and Mission Director

## Progress of Approved AHP Projects



Completed DUs in Rewa

## Progress of Approved AHP Projects



Completed DUs in Chhindwara

## Progress of Approved AHP Projects



Completed DUs in Khargone

## Progress of Approved AHP Projects




Completed DUs in Damoh

# Progress of Approved AHP Projects


AHP Project at Morena



LIG/MIG DUs of AHP  
Project at Damoh

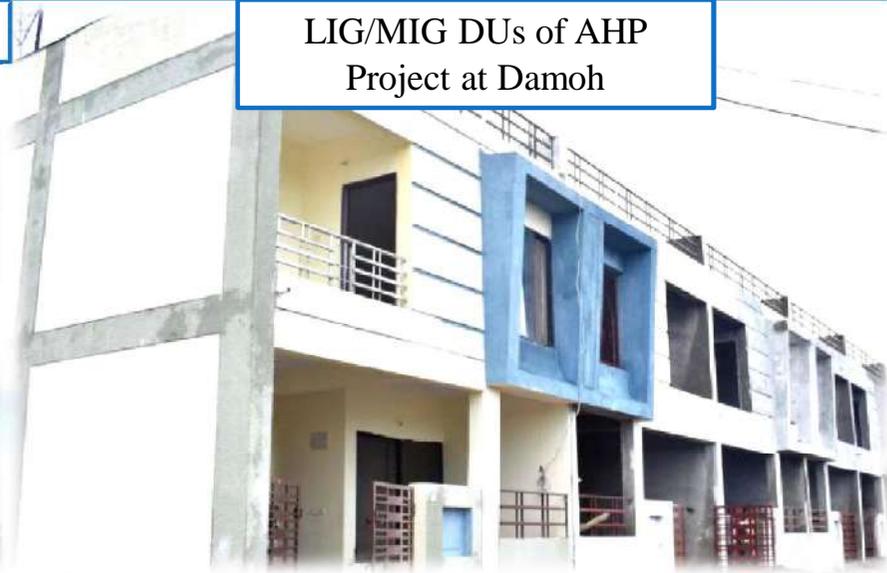

AHP Project at Chhindwara

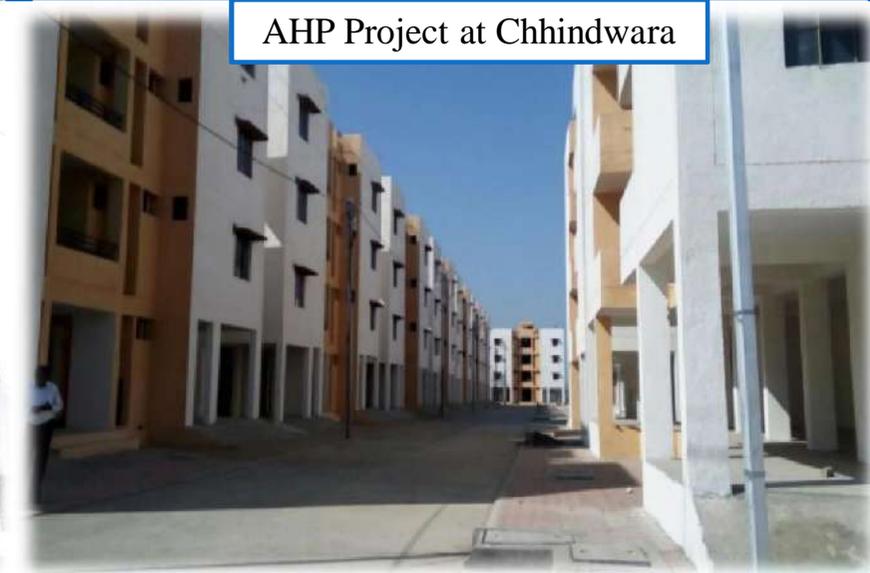


AHP Project at Morena

# Progress of Approved AHP Projects

Completed DUs in Satna (MPHIDB)



Completed DUs in Chhatarpur (MPHIDB)

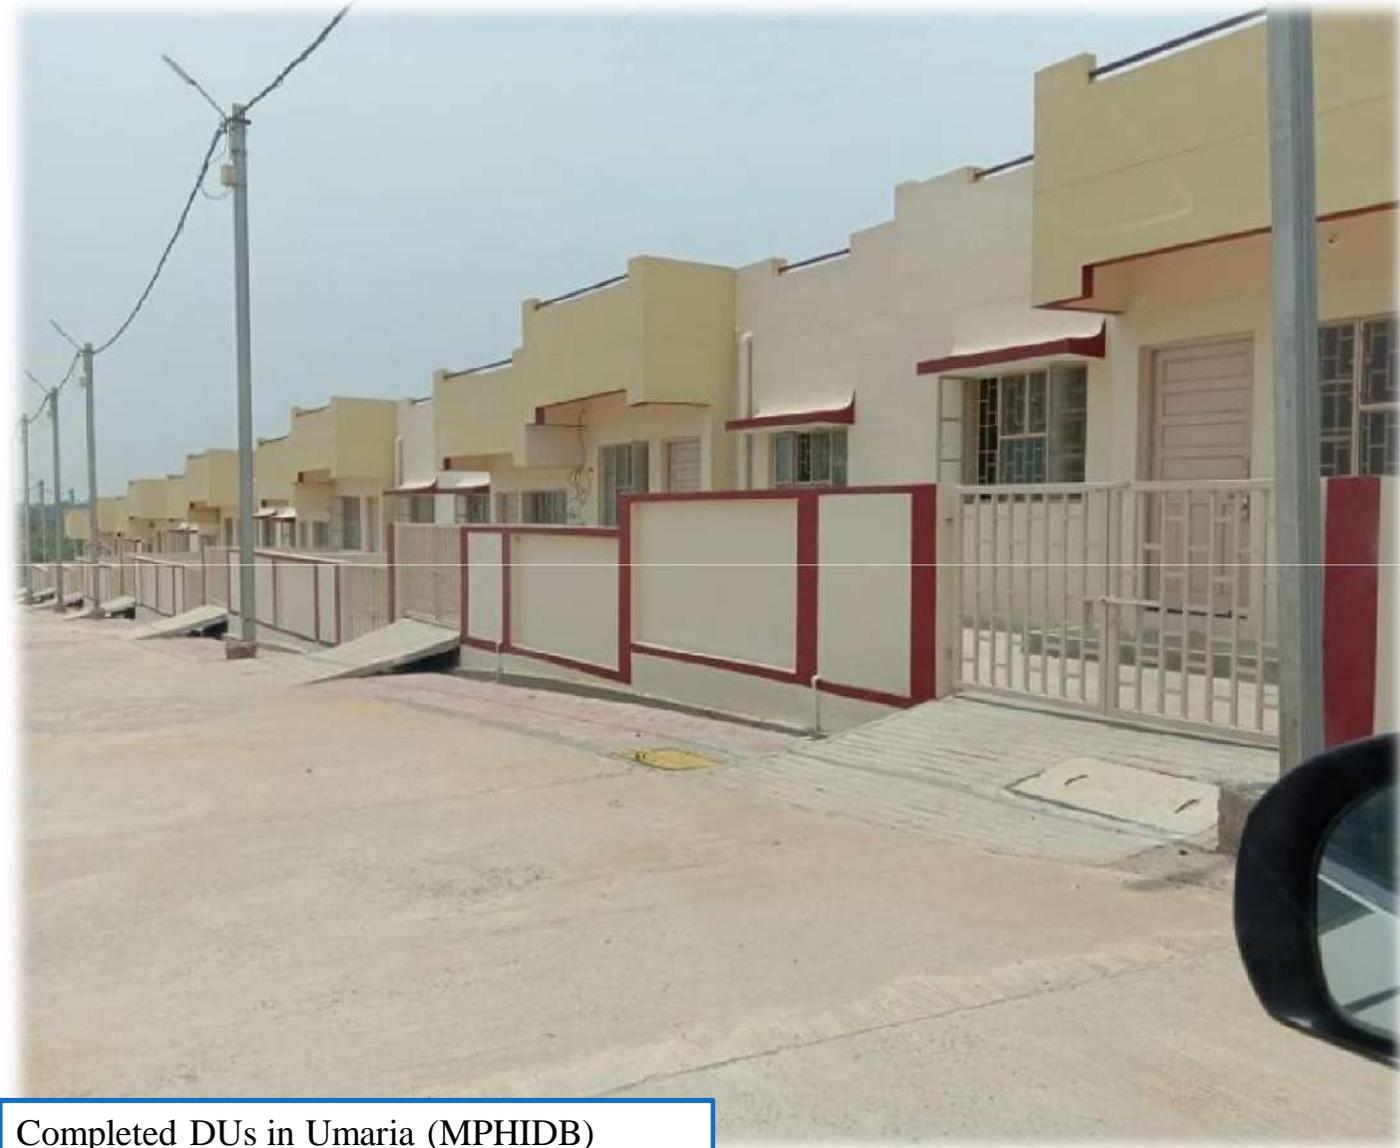

Completed DUs in Umaria (MPHIDB)

## Progress of Approved AHP Projects



Completed DUs in Katni (MPHIDB)

# Photographs Beneficiary Led Construction (BLC)



# Progress of Approved BLC Projects



Completed BLC DUs in Chhindwara & Alirajpur



# Progress of Approved BLC Projects

Chhindwara



Betul



Khandwa



Berasia



Khandwa

Soyatkalan

Katangi

Rehli

# Progress of Approved BLC Projects

Badwani




Sendhwa



Khandwa



Hatod

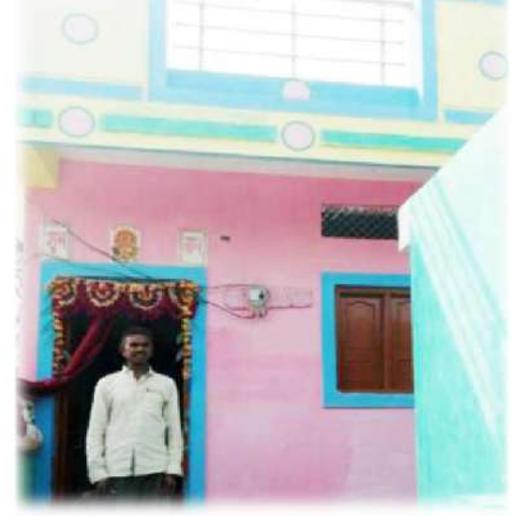

Mandla



Lanjhi



Niwas



## Progress of Approved BLC Projects



## Progress of Approved BLC Projects



# Progress of Approved BLC Projects



Khurai



Rehli



# Progress of Approved BLC Projects

Shahpur



Sendhwa



Suwasra



Rewa



Sehore



Tikamgarh-AHP



# Progress of Approved BLC Projects




Completed BLC DUs in Sendhwa

# Progress of Approved BLC Projects



Multai

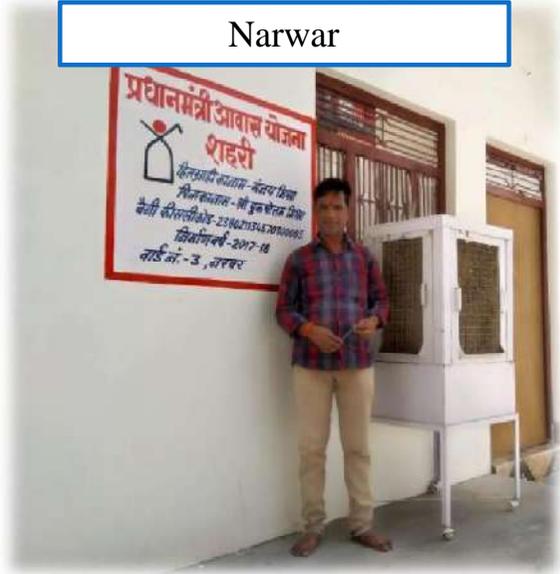

Narwar



Morena



Narsingharh



Morena

# Progress of Approved BLC Projects



Completed BLC DUs in Ujjain

# Progress of Approved BLC Projects

Mandsaur



Completed BLC DUs in Chhindwara



Hoshangabad



## Progress of Approved BLC Projects



BLC DUs in Barwani

# Progress of Approved BLC Projects

Mandsaur



Completed BLC DUs in Ujjain



# Implementation of Angikaar Campaign in Madhya Pradesh



# Implementation of Angikaar Campaign in M.P.



Rangoli made by Students in Joura

# Implementation of Angikaar Campaign in M.P.

Door-to-Door Need Assessment




Plantation & Pledge



Children's Day celebrated in Anganwadi's

# Implementation of Angikaar Campaign in M.P.

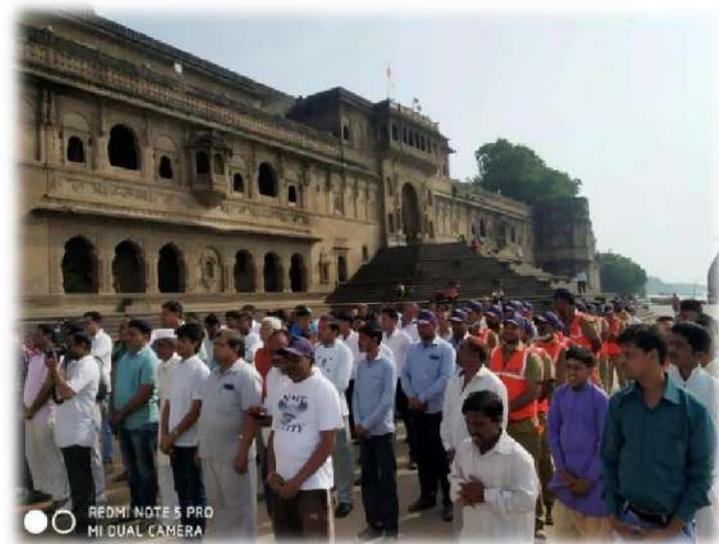

"Swachh Bharat" Pledge on the Ghat of Maheshwar

# Implementation of Angikaar Campaign in M.P.



Need Assessment in Rewa

Rangoli made by Students in Gotegaon

# Implementation of Angikaar Campaign in M.P.



Health Camp in Waraseoni

# Implementation of Angikaar Campaign in M.P.



Awareness Camp in Government School of Patan

# Implementation of Angikaar Campaign in M.P.



Awareness Camps in Indore

# Implementation of Angikaar Campaign in M.P.



Rally at Mandsaur

# Implementation of Angikaar Campaign in M.P.



Wall Painting at Gotegaon

# Implementation of Angikaar Campaign in M.P.



# Implementation of Angikaar Campaign in M.P.



Gwalior Division



Mungaoli, Ashoknagar



Ujjain Division



Sagar Division



Indore Division



Bhopal Division

**Thank You...**
