Pradhan Mantri Awas Yojana (PMAY-U)



Proposal for 04 projects with 1756 EWS Houses under Vertical-3 AHP Proposal for 354 projects with 170178 validated Beneficiaries under Vertical 4 – BLC (N) Proposal for 60 projects with 7281 validated Beneficiaries under Vertical 4 – BLC (E)

Presented to 43rd CSMC Dated 25-02-2019



State Urban Development Agency (SUDA), Government of Uttar Pradesh

PROGRESS OF PMAY (U)



Indicators	Current Status (No.)
■ Cities Approved	653 Nos
■ Total Application Received after De duplication	27,64,203
 Total Physical Validation completed in ULB's Total no of Applications physically Validated Demand Survey Completed . SECC 2011 data linkage 	635 ULBs 24,61,462 635 ULBs 28% average
Cases accepted/rejected (including deduplication)	19,48,395/7,86,080
■ Whether HFAPoA Submitted	136 HFAPoA submitted to MoHUA
■ Whether AIP Submitted	Yes
■ Whether HFAPoA & AIP entered in MIS	Under Progress
 SLTC/CLTC staffs approved vs. placed 	SLTC — 06 and CLTC — 75
■ State Budgetary Provision for PMAY (U)	2217.24 Cr. ₂



STATUS OF MANDATORY CONDITIONS

Mandatory conditions	Current Status
Dispensing the need for separate Non Agricultural (NA) Permission	Complied
Prepare/amend their Master Plans earmarking land for Affordable Housing	Under Progress
Single-window, time bound clearance for layout approval and building permissions	Complied
Adopt the approach of deemed building permission and layout approval on the basis of pre-approved lay outs and building plans.	Complied
•Amend or legislate existing rent laws on the lines of the Model Tenancy Act.	Under Progress
 Additional Floor Area Ratio (FAR)/Floor Space Index (FSI)/ Transferable Development Rights (TDR) and relaxed density norms. 	Provision for Additional FAR / FSI done and TDR is under process

INTERFACE WITH MIS



Indicators	Current Status (No.)
■Projects approved:	2473
■Projects entered (7A/B/C/D)	2473
■DUs approved under BLC	7,99,598
Beneficiaries attached	6,63,230
■Houses geo-tagged	3,16,813
■Total fund transferred through DBT (Rs. Lakhs)	3,43,474.55
■National Electronic Funds Transfer (NEFT)	-
■PFMS/ DBT	In BLC vertical, Rs 3434.75 Cr. released to 2,20,604 beneficiaries through PFMS portal and in AHP vertical, Rs. 255.98 Cr. released to different development authorities and Awas Vikas Parishad, Lucknow as Ist instalment
■Aadhar Payment Bridge (APB)	

PROGRESS OF PROJECTS



Verticals	Houses Approved	Tendered	Work Grounded/In Progress order					Completed
			Issued	Foundati on	Lintel	Roof Casted	Total	
ISSR	-	-	-	-	-	-	-	-
AHP	128,093	29,920	26,256	14,065	-	4,559	18,624	110
BLC (N/E)	7,99,598	3,16,813	3,16,813	1,76,688	23,945	37,781	2,38,414	78,399
Total	9,27,691	3,46,733	3,43,069	1,90,753	23,945	42,340	2,57,038	78,509
CLSS Till 24.02.2019, upfront subsidy of Rs 483.28 Cr. released to 23,102 beneficiaries.								

Note: Provide the details of relevant projects

PROJECT PROPOSAL BRIEF for

Verified Beneficiaries



Verticals	ISSR	AHP	BLC (New)	BLC (E)	Total
■No. of Projects	-	4	336+18 = 354	50+10 = 60	390 + 28 = 418
■No. of DUs	-	1,756	164,399 + 5,779 = 1,70,178	6,346 + 935 = 7,281	1,72,501 + 6,714 = 1,79,215
■Project Cost in Lakh	-	10846.69	6,04,533.98 + 20,098.13 = 6,24,632.11	15,208.69 +1963.19 = 17,171.88	6,30,589.36 + 22,061.32 = 6,52,650.68
■Central Share in Lakh	-	2,634.00	2,46,598.50 + 8,668.50 = 2,55,267.00	9,519.00 + 1206.00 = 10,725.00	2,58,751.5 + 9,874.50 = 2,68,626.00
■State Share in Lakh	-	1,756.00	1,64,399.00 + 5,779.00 = 1,70,178.00	5,661.04 + 879.03 = 6,540.07	1,71,816.04 + 6,658.03 = 1,78,474.07
■ULB/ IA Share in Lakh	-	2,944.93	0	0	2,944.93
■Beneficiary Share in Lakh	-	3,511.76	1,93,556.48 + 5,650.63 = 1,99,207.11	28.65 + 4.41 = 33.06	1,97,096.89 + 5655.04 = 202751.93

Verticals	Per Unit Cost	Central Share	State Share	ULB/ IA Share	Benf. Share	Completion Time
■ AHP Project	4.50	1.50	1.00	2.50	2.00	18-24 Months
■BLC N - Zone2 & Zone 3	3.36	1.50	1.00	-	0.86	15 Months
■BLC N – Zone3 (BCS) & Zone 4	3.80	1.50	1.00	-	1.30	15 Months 6

PROJECT PROPOSAL BRIEF for

Verified Beneficiaries



Verticals	ISSR	AHP	BLC (New)	BLC (E)	Total
■No. of Projects	-	4	354	60	418
■No. of DUs	-	1,756	1,70,178	<i>7</i> ,281	1,79,215
■Project Cost in Lakh	-	10846.69	6,24,632.11	17,171.88	6,52,650.68
■Central Share in Lakh	-	2,634.00	2,55,267.00	10,725.00	2,68,626.00
■State Share in Lakh	-	1,756.00	1,70,178.00	6,540.07	1,78,474.07
■ULB/ IA Share in Lakh	-	2,944.93	0	0	2,944.93
■Beneficiary Share in Lakh	-	3,511.76	1,99,207.11	33.06	202751.93


Verticals	Per Unit Cost	Central Share	State Share	ULB/ IA Share	Benf. Share	Completion Time
■ AHP Project	4.50	1.50	1.00	2.50	2.00	18-24 Months
■BLC N - Zone2 & Zone 3	3.36	1.50	1.00	-	0.86	15 Months
■BLC N - Zone3 (BCS) & Zone 4	3.80	1.50	1.00	-	1.30	15 Months 7


PROJECT PROPOSAL BRIEF for EWS Houses under AHP Vertical




04 Projects in 04 Districts comprising 1,756 EWS Dwelling Units under AHP was recommend for the approval by SLAC held on 22-02-19.


#	Authority Name	District	Nos. of EWS DUs	Central Share	State Share	Ben. Share	IA Share	Project Cost
1	UP Housing and Development Board	Banda	240	360.00	240.00	480.00	576.00	1,656.00
2	UP Housing and Development Board	Kanpur Dehat	480	720.00	480.00	960.00	1,051.20	3,211.20
3	M/S Shri Jee Housing Pvt. Ltd. (Consortium) (Hapur-Pilkhuwa Development Authority)	Hapur	480	720.00	480.00	959.76	1,150.93	3,310.69
4	M/S Amit Goel (Allahabad Development Authority)	Allahabad	556	834.00	556.00	1,112.00	166.80	2,668.80
	Total		1756	2,634.00	1,756.00	3,511.76	2,944.93	10,846.69

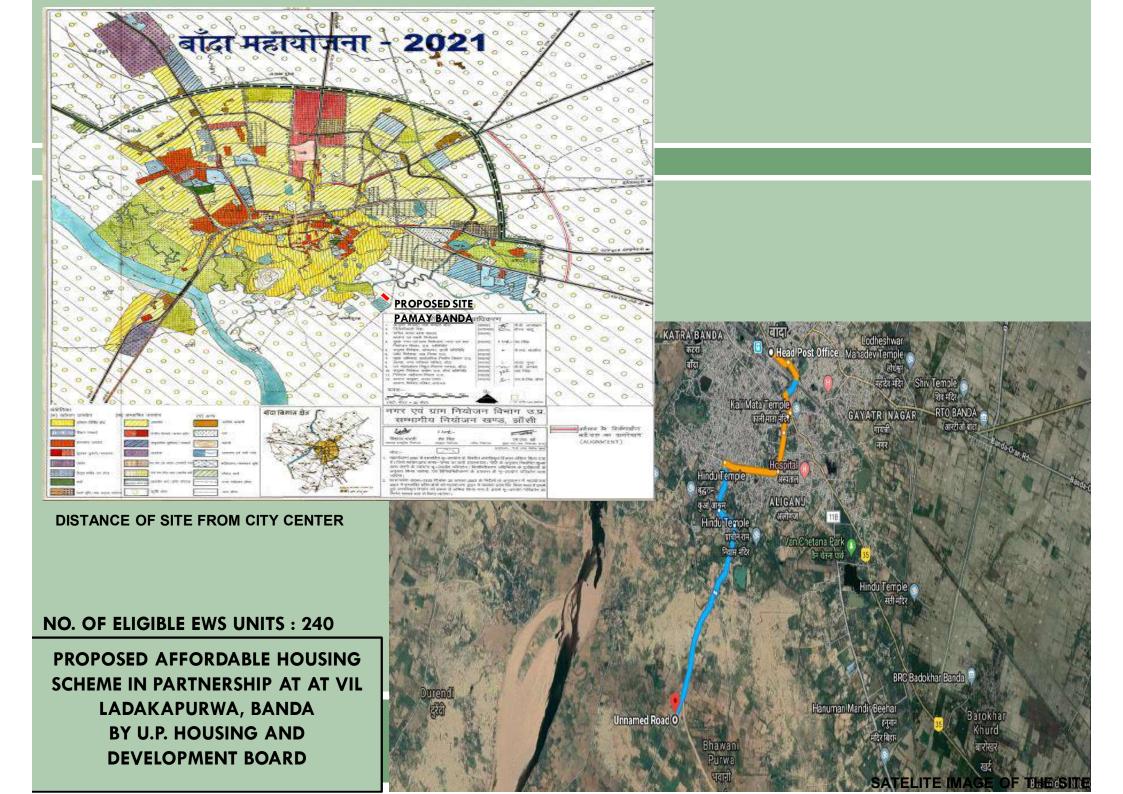



CLUSTER PLAN

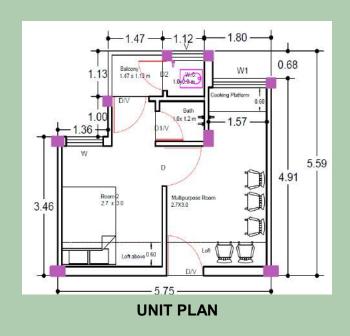


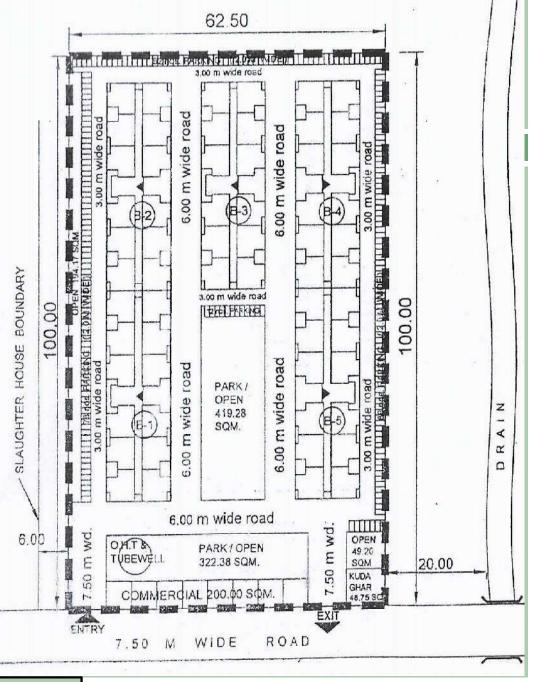


PROPOSED AFFORDABLE HOUSING SCHEME IN PARTNERSHIP AT AT VIL LADAKAPURWA, BANDA BY U.P. HOUSING AND DEVELOPMENT BOARD

SITE PLAN


NO. OF ELIGIBLE EWS UNITS: 240

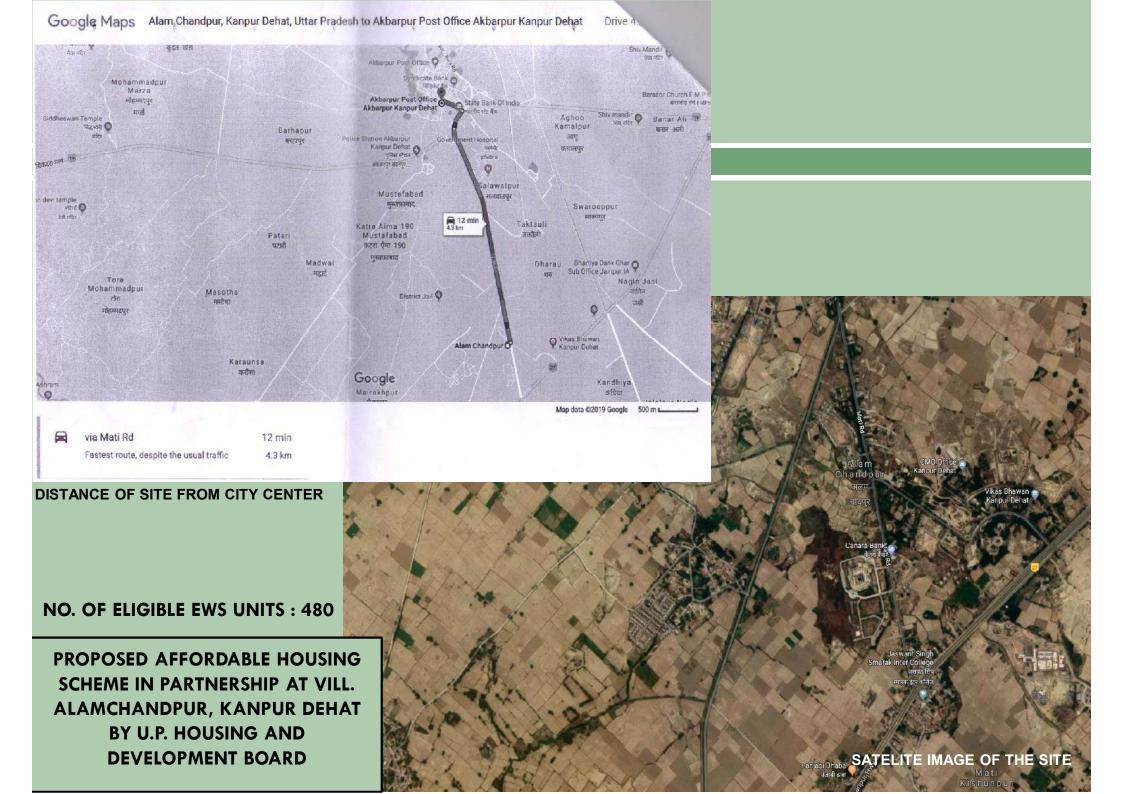

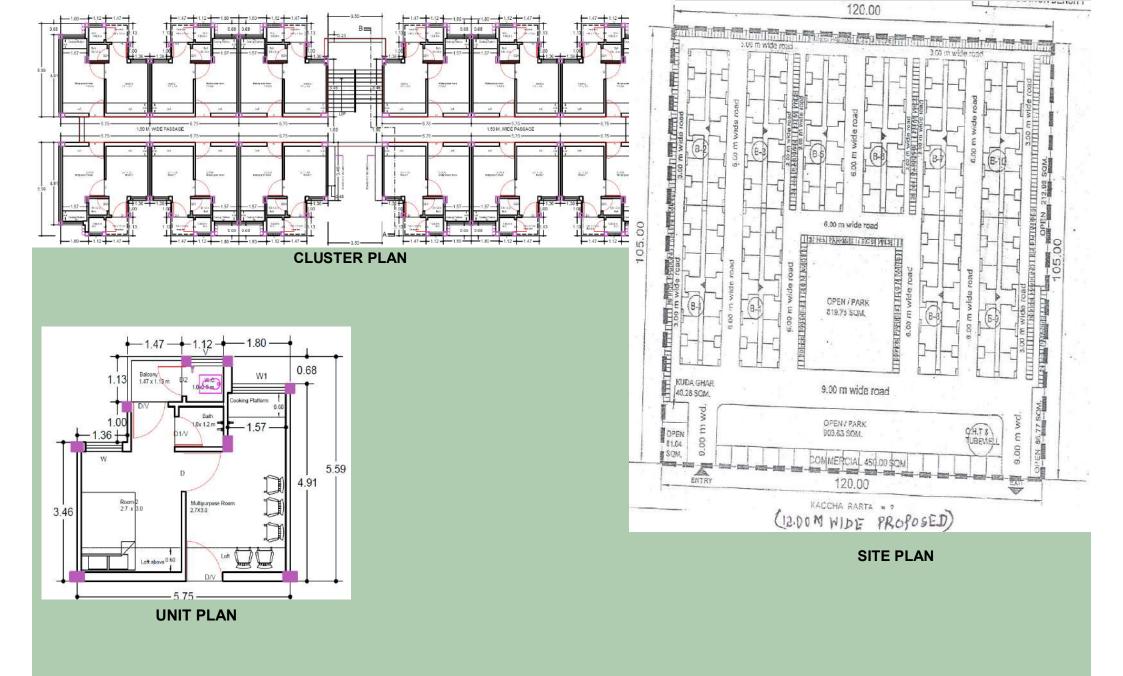

PROPOSED AFFORDABLE HOUSING SCHEME IN
PARTNERSHIP AT VILL. ALAMCHANDPUR, KANPUR DEHAT
BY U.P. HOUSING AND DEVELOPMENT BOARD

NO. OF ELIGIBLE EWS UNITS: 480

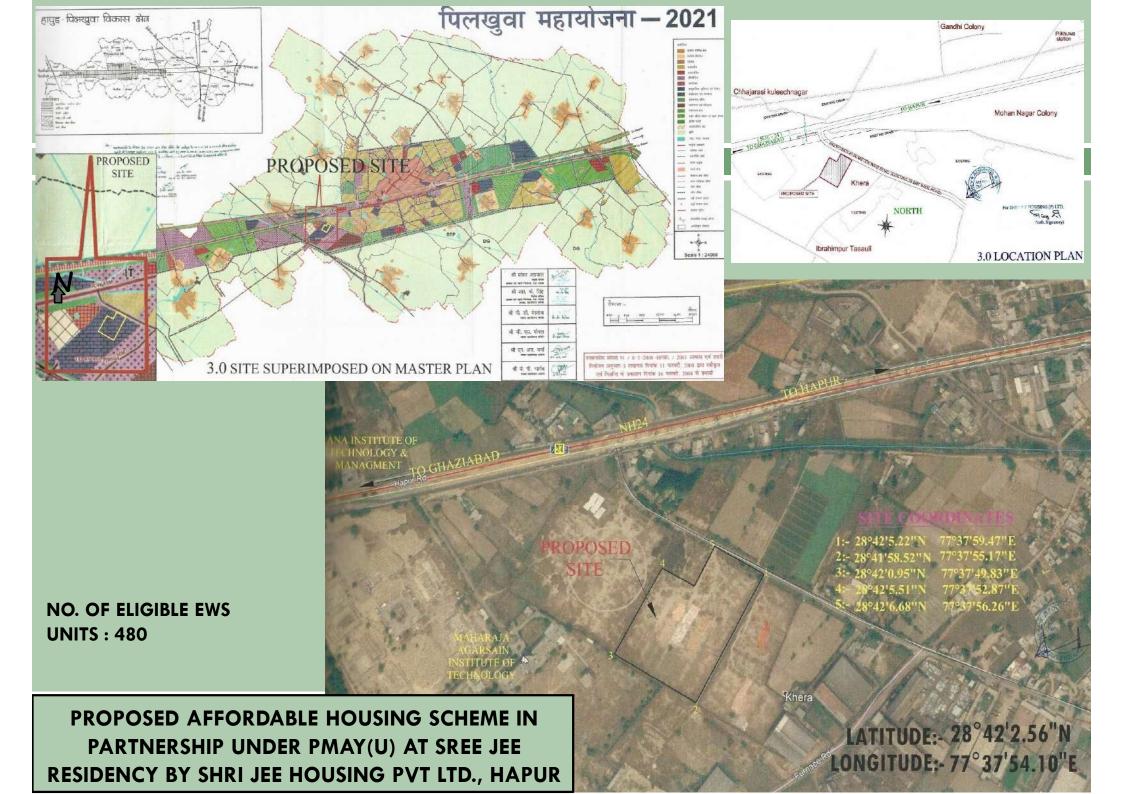





UNIT PLAN

Carpet Area: 23.00 SQ.


MT.

CLUSTER PLAN

NO. OF ELIGIBLE EWS UNITS: 480

PROPOSED AFFORDABLE HOUSING SCHEME IN PARTNERSHIP UNDER PMAY(U) AT SREE JEE RESIDENCY BY SHRI JEE HOUSING PVT LTD., HAPUR



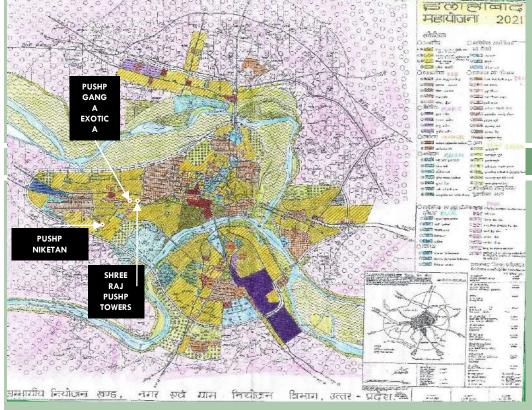







NO. OF ELIGIBLE EWS UNITS: 556

PROPOSED AFFORDABLE HOUSING SCHEME IN PARTNERSHIP AT PUSHPA NIKETAN, PUSHPA GANGA AND SHREE RAJ PUSHP, ALLAHABAD










NO. OF ELIGIBLE EWS UNITS: 556

PROPOSED AFFORDABLE HOUSING SCHEME IN PARTNERSHIP AT PUSHPA NIKETAN, PUSHPA GANGA AND SHREE RAJ PUSHP, ALLAHABAD



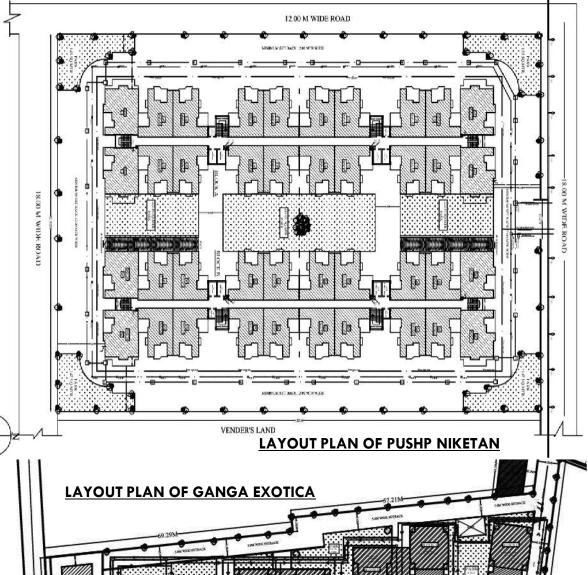


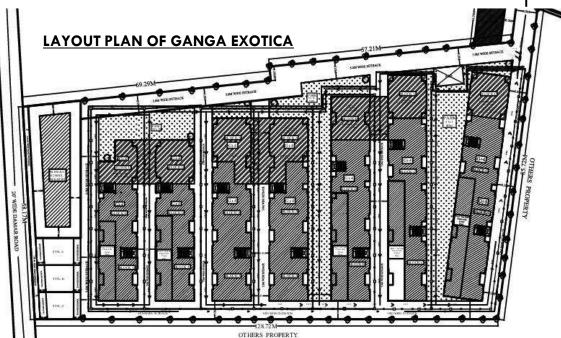

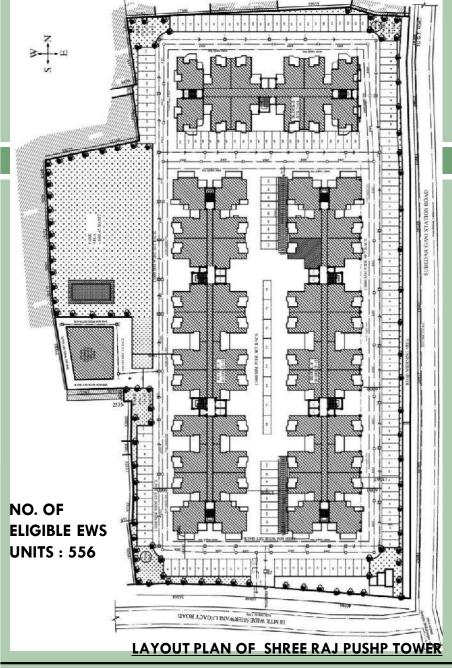

PROPOSED AFFORDABLE HOUSING SCHEME IN PARTNERSHIP AT PUSHPA NIKETAN, PUSHPA GANGA AND SHREE RAJ PUSHP, ALLAHABAD



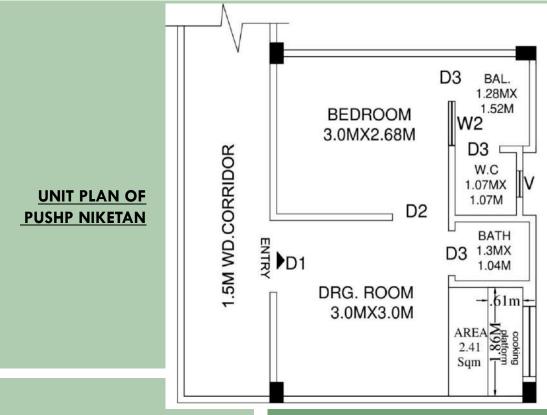

Carpet Area: 22.789

CLUSTER PLAN OF PUSHP NIKETAN

NO. OF ELIGIBLE EWS UNITS: 556

PROPOSED AFFORDABLE HOUSING SCHEME IN PARTNERSHIP AT PUSHPA NIKETAN, PUSHPA GANGA AND SHREE RAJ PUSHP, ALLAHABAD

PROJECT PROPOSAL BRIEF for Verified Beneficiaries under BLC(N)



336 Projects in 60 districts comprising 1,64,399 validated Beneficiaries under BLC(N) was recommended for the approval.

Amount in Lakh

Earth Quake Zone Classification	Proposed DUs under BLC (N)	Central Share (1.5L)	State Share (1L)	Beneficiary Share	Total Cost
Zone -III	46,379	69,568.50	46,379.00	39,834.62	1,55,782.12
Zone –IV	1,14,955	1,72,432.50	1,14,955.00	1,49,711.67	4,37,099.17
<u>BCS</u>	3,065	4,597.50	3,065.00	4,010.19	11,672.69
Total	1,64,399	2,46,598.50	1,64,399.00	1,93,556.48	6,04,553.98

Cost of DU in Zone II/Zone III – 3.36 Lakh & Cost of DU in BCS & Zone IV – 3.80 Lakh

PROJECT PROPOSAL BRIEF for Verified Beneficiaries under BLC(E)



50 Projects in 19 districts comprising 6,346 validated Beneficiaries under BLC(E) was recommended for the approval .

Earth Quake Zone Classification	Proposed DUs under BLC (E)	Central Share (1.5L)	State Share (upto 1L)	Beneficiary Share	Total Cost
Zone -III	1,059	1,588.50	977.09	28.65	2,594.24
Zone -IV	5,287	7,930.50	4,683.95	0.00	12,614.45
Total	6,346	9,519.00	5,661.04	28.65	15,208.69



PROJECT PROPOSAL BRIEF

Checklist	Status (Y/N)
■Layout plan(as per NBC norms) Attached	Yes, attached
SLAC/SLSMC approval/Minutes submitted	SLAC approval on 21/02/19 & 22/02/19 AND SLSMC approval on 22/02/19
■Land title status (encumbrance free)	Yes for 1,70,745 Beneficiaries
■Beneficiary list (BLC) submitted	Yes
■No. of Beneficiaries with Aadhar ID	1,70,745 Nos
■No. of Beneficiaries with other Unique ID	-
■No. of Aadhar seeded Bank accounts	-
Status of physical & social infrastructure	Provisions will be made at ULB Level
Implementation plan/Completion period	15 Months
■Beneficiary consent sought	Yes

PROPOSAL for Submission of Housing For All Plan of Action(HFAPoA)



61 Housing for All Plan of Action (HFAPoA) of 12


Districts (Balrampur, Basti, Bhadohi, Etawah, Hathras, Jhansi,

Kanpur Nagar, Lucknow, Muzaffar Nagar, Raibareilly, Sambhal

and Sultanpur) under PMAY(U).

Proposed DU Layout Plan & Room Sizes under BLC(N)



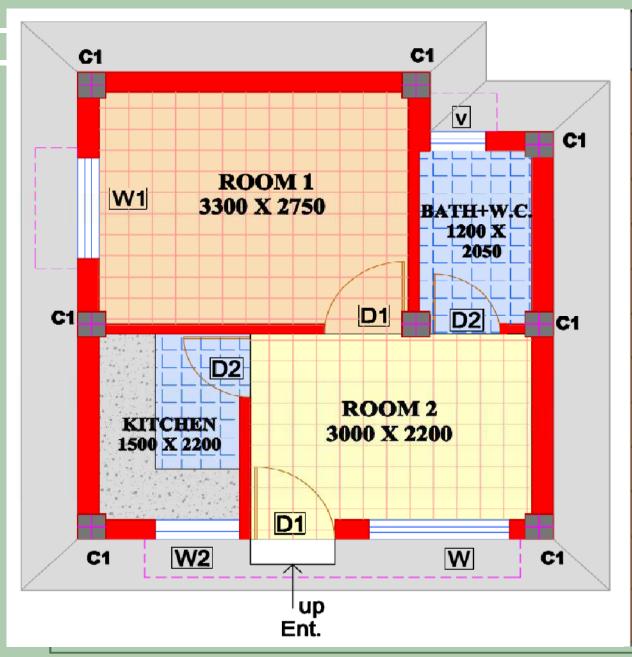

AREA STATEMENTS

SL.	DESCRIPTION	LENGHT	WIDTH	AREA (SQ.M.)					
1.	ROOM1	3.30	2.75	9.075					
		0.90	0.115	0.104					
2	ROOM2	3.00	2.20	6.800					
		0.90	0.23	0.207					
3.	KITCHEN	1.50	2.20	3.300					
		0.75	0.115	0.086					
4,	BATH+W.C.	1.20	2.05	2.480					
		0.75	0.115	0.086					
	DEDUCTION OF	- 0.0392							
	C	21.77							
	BUILT AREA 27.110								

Completed Houses under PMAY(U) in District Varanasi



Sheela Devi W/o Ramji Sonkar 18/58,Hall Gaon Jaitpura,Pahadiya Varanasi



Malti Devi W/o Nand Lal Maurya 18/56,Hall Gaon Jaitpura,Pahadiya

Varanasi

Completed Houses under PMAY(U) in District Ghaziabad



Akhtar S/o Summi Khan 148,Roji Nagar,Vijay Nagar Ghaziabad



Ganga W/o Kartar Singh Ward No 10,Murad Nagar Ghaziabad

Completed Houses under PMAY(U) in District Bullandshahar




Geeta W/o Anil Kumar Moh-Devipura Bullandshahar




Balmukund Singh S/o Lekh Raj Singh
Moh-Devipura
Bullandshahar

Completed Houses under PMAY(U) in District Rampur

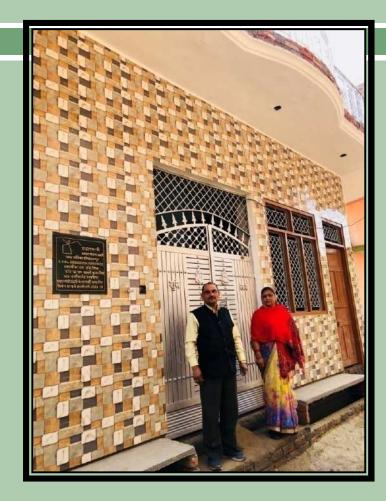

Radha Mishra W/o Ashwani Kumar Bhamrauwa Panvadiya, Rampur

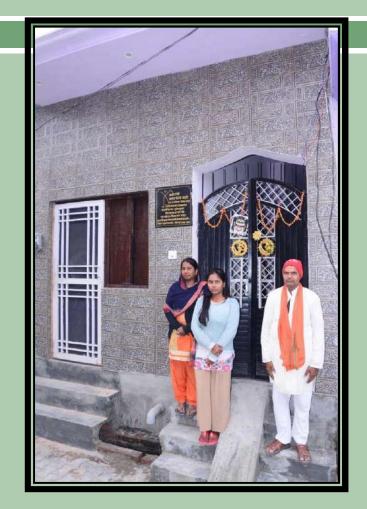

Sunil KumarS/o Ram Nath Gaur Ward No-8,Vikas Nagar Rampur

Completed Houses under PMAY(U) in District Jalaun & Jhansi



Naseema W/o Muin Naya Patel Nagar Orai, Jalaun



Mukhtar Ahmad S/o Fazal Ahmad 198,Ward No.4,Azad Nagar, Bhattagaon,Jhansi

Completed Houses under PMAY(U) in District Unnao



Satyendra Tripathi S/o Munna Lal Tripathi Indira Nagar,Hydrabad Unnao



Amar Singh S/o Chota Singh Ward No.10,Indira Nagar, Hydrabad,Unnao

Tentative Road Map - 2022



Year		Total in			
1eai	BLC(N/E)	AHP	ISSR	CLSS	Lakh
2017-18	2.00	2.00	ó	1.00	5.00
2018-19	2.00	1.50	0.20	1.00	4.70
2019-20	0.50	1.00	ó	1.00	2.50
2020-21	ó	ó	ó	1.00	1.00
2021-22	ó	ó	ó	1.00	1.00
Total	4.50	4.50	0.20	5.00	14.20

Note:-

ÉTarget of AHP component is related to Housing Department, Govt of UP.

ÉTarget of ISSR component depend on consent of tenable slum dwellers on the Govt. Land.

ÉTarget of CLSS component depends upon the loan sanctioning by banks / PLIs and for this component HUDCO and NHB.

BEST PRACTICE/ INNOVATION



Innovative technology Adopted

Best practice to be shared

- 1. Systematic approach has been adopted for demand survey.
- 2. Provision of giving fund of **Rs 0.50 Lac** to beneficiaries of BLC vertical as **1**st **installment** at zero level for construction of their house.

Details of IEC initiatives

- 1. Organization of workshops at State Level, District Level an ULB Level.
- 2. Organization of Awareness camps at community level for better participation.
- 3. Frequent Newspaper Advertisement regarding demand survey under PMAY (U) and its benefits.
- 4. Verification of beneficiary through Call center.

RAY – AT A GLANCE

Financial Status -

								(Amt in Cr.)	
	project Approved	No of cities covered	Total Project Cost	ACA Committed	ACA released	Total fund released by SUDA (CS+SS)	Total Expenditure against fund released	UC sent to Gol	
1	.8	16	574.26	279.22	172.67	304.01	239.55	189.46	

RAY – AT A GLANCE

Physical Status -

project Approved	DUs Sanctioned	DUs Type	DUs Completed	DUs in Progress	DU Occupied	DUs Unoccupied
18	8409	IN-SITU / Relocation	4607	414	4607	0

Progress of ray - Pokhar Purva slum of Kanpur (Housing)







Progress of ray - Jhansi (Housing)



Progress of BSUP-IHSDP

Physical Progress

S. No.	Scheme Name	Total Sanction Project	No. of DUs		Phy	ysical Progr	ess		Completion Certificate		
		. 10,000	Sanction DUs	After Surrender	DUs Complete d	DUs in Progress	DUs Allotted	Occupied		Sent to Gol	
1	2	3	4	5	6	7	8	9	10	11	
1	BSUP	69 / 67	68217	45599	43002	2597	45170	38851	6	6	
2	IHSDP	164 / 159	47399	37818	34818	3000	30637	27969	26	26	
	Total	233 / 226	115616	83417	77820	5597	75807	66820	32	32	

Financial Progress (Amt. in cr.)

S. No.	Scheme Name	Project Cost		Amount of ACA		Release ACA to be amount of refund	ACA to be		Balance ACA to be	Total UC sent	Balance UC
No.		Sanction	After Surrender	Sanction	After Surrender	ACA			refund	1 - 1	
1	2	3	4	5	6	7	8	9	10	11	12
1	BSUP	2353.80	1637.66	1149.04	798.03	876.31	78.28	78.28	0.00	736.83	61.20
2	IHSDP	1325.10	987.67	845.76	624.41	718.19	93.78	93.78	0.00	589.95	34.46
	Total	3678.90	2625.33	1994.80	1422.44	1594.50	172.06	172.06	0.00	1326.78	95.66

PROGRESS OF BSUP & IHSDP









MEERUT













